APPLICATION MODERNIZATION

Blueprint — internal reference

A Assessment · B Migration · C Platform Ops · on-prem applications to Kubernetes on Google Cloud or Azure

1 **Positioning and commercial logic**
Package summary, commercial logic, evidence and status, target customers, scope boundary.
p. 2 – 6

2 **Method and architecture**
Method, 6R classification, complexity model, target architecture on Google Cloud and Azure, technology mapping.
p. 7 – 12

3 **Delivery**
Assessment, Migration and Platform Ops, pricing options, team, sizing and effort, acceptance criteria.
p. 13 – 19

4 **Follow-on and status**
Follow-on map, risks and open points, verification summary.
p. 20 – 22

Package Summary — What, for Whom, When

KOMTAS

On-prem applications moved to containers on Kubernetes in the cloud, in waves, and operated monthly. Source: internal meeting with Güner Hacıoğlu (Cloud Solutions), 15.10.2026.

01 · SUMMARY

WHAT IT IS

Inventory and classification

application list, 6R route and complexity class per application

Containers on Kubernetes

replatform to GKE or AKS with Terraform, Helm and Argo CD

Migration in waves

pilot application first, then waves, cutover and hypercare

Platform operations

monthly cluster and GitOps operations, upgrades, incidents

THREE TIERS

A — Assessment

inventory, 6R and complexity, target architecture, wave plan, B estimate

3–4 weeks by band, fixed fee «GÜNER DOĞRULASIN»

B — Migration

platform foundation, pilot, waves, cutover; unit price or capped T&M

effort from the A inventory «GÜNER DOĞRULASIN»

C — Platform Ops

monthly cluster and GitOps operations, upgrades, incidents

monthly, min. 12 months «GÜNER DOĞRULASIN»

BASIS — KNOWN FACTS

- On-prem applications containerised and moved to cloud at Ecofin
- Stack used: Kubernetes, Terraform, Helm, Argo CD
- Delivered by the Komtaş cloud team
- Seen as a critical capability that can be packaged
- Komtaş is a Google Cloud Premier partner
- Azure partnership completed

Status: draft. Built from one meeting (15.10.2026) and candidate note aday-23. Durations, efforts, complexity criteria, bands and acceptance thresholds are drafts. Every drafted item carries the orange verification tag and is listed for Güner Hacıoğlu's review (p. 22).

Commercial Logic — Profit Comes from Migration and Operations

internal only

KOMTAS

Internal only. Margin figures never appear in the customer deck or in the proposal templates.

CONSUMPTION MARGIN · INTERNAL

PROVIDER	CONDITION	MARGIN
Google	Premier partner, base	12%
Google	with incentives and funds	13–15%
Google	large deals	~5–6%
Azure	starting level	3%

Thin consumption margin.
Migration moves workloads to GKE or AKS and consumption grows, but the margin on it is thin. Consumption growth is an indirect result, not the business case.

WHERE THE PROFIT IS

Cloud consumption
thin margin, grows indirectly

↓

A Assessment
fixed fee, opens the account

↓

B Migration
largest service revenue

↓

C Platform Ops
recurring monthly revenue

B and C carry the profit. An assessment that does not lead to B leaves most of the value unsold.

PRICING RULES

1. A is a fixed fee by band
2. B has no turnkey fixed price: unit price per application by class, or capped T&M
3. C is a monthly fee for a fixed hour capacity with a minimum term
4. Each A proposal names the B and C step that follows

Open: fee levels. Day rates, unit prices per class, the T&M cap and the monthly fee for C are not set. Fees are not part of this blueprint.

Evidence and Status

KOMTAS

What the package rests on today. Internal only: the customer is named here and in the input forms, never in customer-facing files.

01 · EVIDENCE

EVIDENCE

Ecofin

On-prem applications moved to Kubernetes

Containerised and moved to cloud with Kubernetes, Terraform, Helm and Argo CD by the Komtaş cloud team. Named in the meeting as a critical capability to package.

«NUMBER»

Applications moved at Ecofin

Application count, target cloud, duration and team are not yet recorded.

STACK AT ECOFIN

Kubernetes container orchestration	delivered
Terraform infrastructure as code	delivered
Helm application packaging	delivered
Argo CD GitOps deployment	delivered
Cluster service and cloud GKE, AKS or other «...»	to confirm
CI/CD and observability tools «...»	to confirm

Delivery capacity: cloud team, not the SAT data / AI core.

STATUS AND RISK

Delivery capacity (S11)

Delivery sits in the cloud team. Selection criterion S11 depends on how many cloud engineers can run Kubernetes migrations.

Outside the 360 layers

The package moves the application layer; it does not sit in Data / Analytic, Context, Agent or Action 360.

Single reference (S1)

One customer so far. Open modernization opportunities from Sales: «NUMBER».

Customer naming. Customer deck and proposals do not name Ecofin. They use the anonymous line "an on-prem application estate moved to Kubernetes on Google Cloud" with a verification tag until use of the name and sector is approved.

Target Customers and Triggers

KOMTAS

Who is approached and on what occasion. Profiles and triggers are drafted; they are not drawn from recorded deals.

TARGET CUSTOMER PROFILES «GÜNER DOĞRULASIN»

Company with an on-prem application estate
in-house or custom applications on VMs in its own data centre

Data centre exit or hardware renewal due
a date that forces a decision

Team with slow, manual releases
a release takes days and needs several people

Company moving to multi-cloud
Google Cloud and Azure in use or planned

TRIGGERS «GÜNER DOĞRULASIN»

Data centre exit

a contract end or consolidation forces the move by a date.

Hardware or licence renewal

renewing on-prem hardware or platform licences is on the table.

Scaling problems

peaks need capacity that the on-prem estate cannot add quickly.

Slow releases

manual deployments; a release takes days and carries risk.

Multi-cloud move

a second cloud is added, or workloads are split between Google Cloud and Azure.

Entry via Cloud Checkup

Checkup findings can name applications to modernise; they become the start of the A inventory.

First call. Number of applications, where they run, runtimes and databases, environments, target cloud, exit or renewal date. The answers feed the input form (file 3a).

Scope Boundary — What It Is Not

KOMTAS

What the package does not do, and the Komtaş packages it links to without absorbing them.

01 · BOUNDARY

OUT OF SCOPE

- Mainframe applications «GÜNER DOĞRULASIN»
- Functional rewrite or new features «GÜNER DOĞRULASIN»
- Application licence negotiation with vendors «GÜNER DOĞRULASIN»
- Execution of end-user tests (UAT is run by the customer) «GÜNER DOĞRULASIN»
- Changes by third-party software vendors «GÜNER DOĞRULASIN»
- Data warehouse and ETL — separate packages

BOUNDARY TO THE DATA PACKAGES



This package moves the application layer.

etl-migration-gcp moves data pipelines; data-modernization consolidates analytic databases on BigQuery. Application Modernization moves the applications themselves and, as an option, each application's own operational database. Where an estate needs both, the packages are quoted side by side, each with its own scope.

RELATED PACKAGES



Cloud Checkup reviews cloud cost, access and configuration; can name modernization candidates.



ETL / Data Modernization data pipelines and analytic databases; not this package.

Boundary rule. Applications and their own databases: this package. Pipelines, data warehouses and analytic databases: the data packages. Mainframe and functional rewrite: not offered.

Method — From Inventory to Operations

KOMTAS

Six steps. The assessment covers steps 1–4; the migration and the operations service follow from its outputs.

02 · METHOD

1 Inventory

application list from the CMDB or the customer template, owner interviews, dependency mapping

OUTPUT

application inventory

2 6R classification

each application gets one of six routes and a complexity class

OUTPUT

6R route and class per application

3 Target architecture

landing zone, cluster design, IaC and GitOps, security, observability

OUTPUT

target architecture document

4 Wave plan

applications grouped into waves by dependency and class; B effort and cost

OUTPUT

wave plan, B estimate

5 Migration

platform foundation, pilot application, waves, cutover and hypercare

OUTPUT

applications running on Kubernetes

6 Operations

cluster operations, upgrades, GitOps maintenance, monitoring, incidents

OUTPUT

monthly service report

A Assessment · fixed fee

B Migration

C Platform Ops

Steps 1–4 are the assessment; their outputs are the input for the B proposal. A B proposal is not written without the A inventory.

Package focus. Replatform to containers on Kubernetes (GKE or AKS) with Terraform, Helm and Argo CD. Refactor only where needed to run in containers; no functional rewrite.

6R Classification

KOMTAS

Every application in the inventory gets one route. The package executes Replatform; Rehost and Refactor only in a limited way; the other three are classified only.

ROUTES AND HOW THE PACKAGE TREATS THEM «GÜNER DOĞRULASIN»

ROUTE	MEANING	IN THIS PACKAGE	TYPICAL SIGNAL
Rehost	move as is to VMs in the cloud	interim step only, where containers are not yet possible «GÜNER DOĞRULASIN»	OS or runtime dependency blocks containers; exit date close
Replatform	move to containers on Kubernetes with small changes	package focus — executed in B	supported runtime; configuration can be externalised
Refactor	change code or design	limited: configuration externalisation, stateless changes «GÜNER DOĞRULASIN»	session state or local files block scaling
Repurchase	replace with SaaS or a commercial product	classified only	standard function; a SaaS product exists
Retire	switch off	classified only	low use; function duplicated elsewhere
Retain	keep where it is	classified only	regulatory or technical reason to stay

Package focus: Replatform to containers.
Refactor stops at what is needed to run in containers. A functional rewrite is out of scope and is quoted separately if asked.

Classified only.
Repurchase, Retire and Retain are recorded in the inventory with a reason. Any work on them is a separate scope.

Complexity Model — Simple, Medium, Complex

KOMTAS

Each application gets a class in phase P2 of the assessment. The class sets its unit effort in B and its price in option 1.

02 · COMPLEXITY

S Simple

stateless, current runtime

STATE
stateless

DATABASES
none or one

INTEGRATIONS
≤2

RUNTIME / OS
current, supported

LICENCE
no constraint

«GÜNER DOĞRULASIN»

M Medium

stateful or own database

STATE
stateful

DATABASES
own database

INTEGRATIONS
3–5

RUNTIME / OS
current, supported

LICENCE
no constraint

«GÜNER DOĞRULASIN»

C Complex

several databases or legacy

STATE
stateful

DATABASES
several databases

INTEGRATIONS
>5

RUNTIME / OS
legacy runtime or OS dependency

LICENCE
licence constraints

«GÜNER DOĞRULASIN»

Classification rule «GÜNER DOĞRULASIN»

An application takes the highest class that any one of its criteria reaches. Example: stateless, one database, 6 integrations → Complex. Scored from the inventory, interviews and the dependency map.

Where the class is used

- B Phase 3 effort: count per class × unit effort
- Option 1 price: unit price per class
- Wave plan: grouping by class and dependency
- Sizing driver: share of complex applications

Optional database block. An application's own operational database can move with it (Cloud SQL / Azure SQL). Its effort is counted in the optional block, not in the unit effort (p. 15).

Target Architecture — Google Cloud

KOMTAS

Applications run as containers on GKE, built and deployed from Git. Infrastructure is defined in Terraform.

02 · GOOGLE CLOUD «GÜNER DOĞRULASIN»

ON-PREMISES TODAY	applications on VMs and app servers	own databases	manual or scripted releases	local monitoring

DELIVERY · GITOPS	**Git repositories** code, Dockerfiles, Helm charts	**CI/CD** Cloud Build, GitLab, GitHub Actions or Jenkins	**Artifact Registry** container images	**Argo CD** syncs Git to the clusters
RUNTIME	**GKE** clusters per environment	**Helm charts** one release per application	**Cloud Load Balancing** ingress and TLS	**Cloud SQL** app databases, optional
FOUNDATION	**Terraform (IaC)**	**landing zone**	**VPC**	**Secret Manager**
OPERATIONS	Cloud Monitoring and Logging	or Prometheus / Grafana	alerts and dashboards per application	

Everything as code

Infrastructure in Terraform, applications in Helm charts, deployments through Argo CD. A change is a Git commit.

Security baseline

Secrets in Secret Manager, network rules in the VPC, access by role. Details set in A phase P3.

Same pattern, two clouds. Terraform, Helm and Argo CD are the same on Google Cloud and Azure; only the managed services underneath change (p. 11–12).

Target Architecture — Azure Mapping

KOMTAS

The same delivery pattern on Azure. AKS replaces GKE; the tools above and below the cluster keep their roles.

02 · AZURE «GÜNER DOĞRULASIN»

ON-PREMISES TODAY	applications on VMs and app servers	own databases	manual or scripted releases	local monitoring

DELIVERY · GITOPS			
Git repositories code, Dockerfiles, Helm charts	**CI/CD** Azure DevOps or GitHub Actions	**Container Registry** ACR, container images	**Argo CD** syncs Git to the clusters

RUNTIME			
AKS clusters per environment	**Helm charts** one release per application	**Application Gateway** ingress and TLS	**Azure SQL** or PostgreSQL Flexible Server, optional

FOUNDATION	**Terraform (IaC)**	**landing zone**	**VNet**	**Key Vault**

OPERATIONS	Azure Monitor	or Prometheus / Grafana	alerts and dashboards per application

No Azure delivery yet

The only recorded delivery is the Ecofin work (target cloud «...»). The Azure mapping follows the same pattern and needs a first project to confirm it.

What changes

AKS, ACR, Key Vault, Azure Monitor and Application Gateway. Terraform modules change provider; Helm charts and Argo CD stay.

Azure partnership. The Azure partnership is completed. The Azure margin starts at 3% (p. 3); the value is in the service, as on Google Cloud.

Technology Mapping — Google Cloud and Azure

KOMTAS

One row per layer. The last column records what was used at Ecofin; open cells are filled after review.

LAYER → SERVICE PER CLOUD «GÜNER DOĞRULASIN»

LAYER	GOOGLE CLOUD	AZURE	SAME ON BOTH	USED AT ECOFIN
Container platform	GKE	AKS	—	Kubernetes; service «…»
Infrastructure as code	Terraform	Terraform	yes	yes
Application packaging	Helm charts	Helm charts	yes	yes
GitOps deployment	Argo CD	Argo CD	yes	yes
CI/CD	Cloud Build, GitLab, GitHub Actions, Jenkins	Azure DevOps, GitHub Actions	partly	«…»
Container registry	Artifact Registry	Azure Container Registry	—	«…»
Secrets	Secret Manager	Key Vault	—	«…»
Observability	Cloud Monitoring / Logging, Prometheus / Grafana	Azure Monitor, Prometheus / Grafana	partly	«…»
App database (optional)	Cloud SQL	Azure SQL, PostgreSQL Flexible Server	—	«…»
Load balancing / ingress	Cloud Load Balancing	Application Gateway	—	«…»
Network	VPC	VNet	—	«…»

Portable core. Terraform, Helm and Argo CD carry the delivery pattern across both clouds; the managed services are swapped per cloud.


A — Assessment: Flow and Timeline

KOMTAS

Kick-off to read-out in phases P0–P4. Fixed fee by band. Customer joins kick-off, interviews and the read-out.

03 · TIER A

PLAN · BAND M, 3.5 WEEKS «GÜNER DOĞRULASIN»

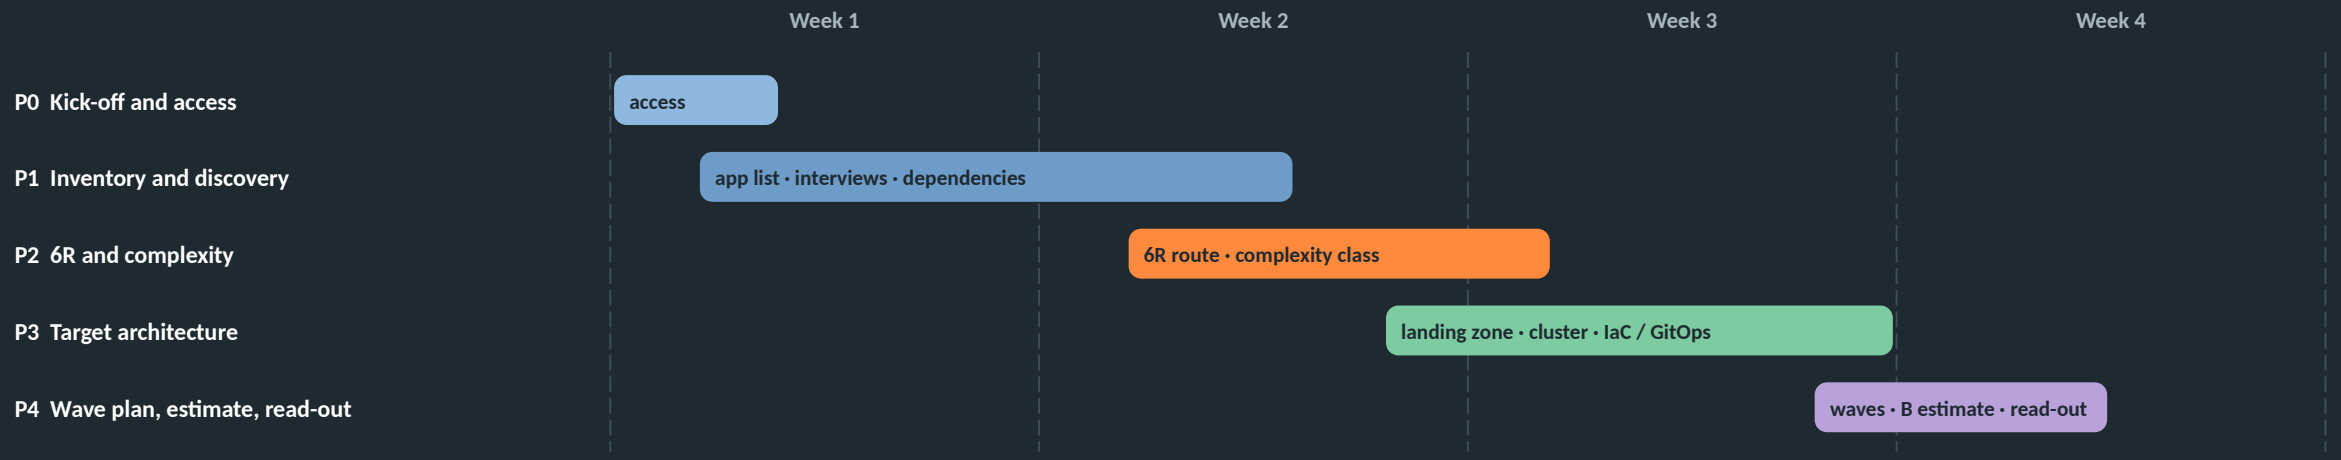

Band S 3 weeks / ~20 pd, band M 3.5 weeks / ~25 pd, band L 4 weeks / ~30 pd. Customer effort 3 / 4 / 5 days. «GÜNER DOĞRULASIN»

ACCESS MODES «GÜNER DOĞRULASIN»

«MOD A» Customer runs

The customer fills the inventory template and runs the agreed discovery commands; outputs are shared.

«MOD B» Read-only access

Komtaş gets read-only access to repositories, VMs and the CMDB and collects the data itself.

DELIVERABLES «GÜNER DOĞRULASIN»

- Application inventory
- 6R and complexity per app
- Target architecture document
- Wave plan
- B effort, cost and team plan
- Risk list

Fixed fee. A is priced by band. Its outputs are the basis for the B proposal; without the A inventory no B proposal is written.

B — Migration: Phases and Effort

no turnkey fixed price

KOMTAS

Phases 1, 2 and 4 are fixed items; Phase 3 follows the inventory. Duration of Phase 3 = effort ÷ number of engineers.

Prerequisite: the A application inventory with 6R route and complexity class per application. Without it, no B proposal is written.

FOUR PHASES

1 Platform foundation

landing zone, cluster(s), Terraform modules, Argo CD, CI/CD templates, observability, security baseline

~30–40 pd «GÜNER DOĞRULASIN»

2 Pilot application

one application end to end; patterns and unit efforts checked

~10–15 pd «GÜNER DOĞRULASIN»

3 Waves

applications moved in waves; each wave tested and cut over

Σ unit effort ÷ engineers

4 Cutover and handover

final cutovers, hypercare, runbooks, handover to the customer or to C

~10 pd «GÜNER DOĞRULASIN»

EFFORT FORMULA

B EFFORT (pd)

Phase 1 + Phase 2 + Σ (apps per class × unit effort) + Phase 4

PHASE 3 DURATION (working days)

Σ (apps per class × unit effort) ÷ number of engineers

SOURCE OF THE FIGURES

counts: A inventory · unit effort: p. 15 · Phase 1: band, p. 18

WORKED EXAMPLE · ILLUSTRATIVE

ITEM	COUNT	UNIT	PD
Simple applications	10	~5 pd	50
Medium applications	7	~12 pd	84
Complex applications	3	~25 pd	75
Phases 1 + 2 + 4 (band M)		35 + 12 + 10	57
B effort total	20 apps		266
Phase 3 with 3 engineers		209 ÷ 3	≈ 70 working days

B — Unit Efforts and Two Pricing Options

KOMTAS

Unit effort per application by class drives Phase 3. Pricing is either a unit price per application or capped time and materials.

UNIT EFFORT PER APPLICATION «GÜNER DOĞRULASIN»

CLASS	UNIT EFFORT	TYPICAL WORK
Simple	~5 pd	container image, Helm chart, pipeline, test support, cutover
Medium	~12 pd	as Simple, plus state or database handling and 3–5 integrations
Complex	~25 pd	as Medium, plus several databases, legacy runtime, licence checks

Unit effort covers analysis, containerisation, deployment, test support and cutover per application.

OPTIONAL — APP DATABASE «GÜNER DOĞRULASIN»

The application's own operational database moves with it to Cloud SQL, or to Azure SQL / PostgreSQL Flexible Server. Counted per database outside the unit effort: «NUMBER» pd per database. Data warehouses and analytic databases are not part of this block.

TWO PRICING OPTIONS · SEPARATE SECTIONS IN PROPOSAL 4b

OPTION 1 — Unit price per application by class

- price per class = unit effort × day rate
- application counts per class from the A inventory
- added applications priced by the same table

OPTION 2 — Capped time and materials

- rate card × team, invoiced monthly
- cap set from the A estimate
- work above the cap only by change request

Phases 1, 2 and 4: fixed items in both options. «GÜNER DOĞRULASIN»

No turnkey fixed price. Proposal 4b carries both options as separate sections; the unused one is deleted before sending.

C — Platform Ops: Monthly Operations

KOMTAS

A monthly hour capacity for operating the clusters and the GitOps pipeline after go-live. Recurring revenue.

03 · TIER C

MONTHLY CAPACITY «GÜNER DOĞRULASIN»

S — **40 h / month**
one cluster, a few applications

M — **80 h / month**
several clusters or environments

L — **160 h / month**
multi-zone or many applications

ACTIVITIES «GÜNER DOĞRULASIN»

- **GKE / AKS operations**
  cluster health, node pools, capacity
- **Version upgrades**
  Kubernetes, add-ons, Helm chart versions
- **GitOps pipeline maintenance**
  Argo CD and CI/CD templates kept working
- **Monitoring and alerting**
  alert rules and dashboards maintained
- **Incident support**
  by priority, within agreed hours
- **Cost follow-up**
  monthly cost view and rightsizing notes
- **Small changes**
  from the monthly capacity

INCIDENT SUPPORT «GÜNER DOĞRULASIN»

Support hours: business hours «...»; 24×7 as an option «...».

P1	**Critical**	production down; response «NUMBER» h
P2	**High**	production degraded; response «NUMBER» h
P3	**Medium**	workaround exists; response «NUMBER» h
P4	**Low**	question or request; response «NUMBER» h

Term. Draft minimum term 12 months. Unused hours are not carried over; work above the capacity is charged at the hour rate. «GÜNER DOĞRULASIN»

Team and Roles

KOMTAS

A Cloud Architect leads A and B with platform and Kubernetes engineers; C is run by a Platform Ops Lead and an engineer. Effort split by role is not yet known.

ROLES «GÜNER DOĞRULASIN»

ROLE	RESPONSIBILITY	A	B	C
Cloud Architect	target architecture, landing zone, design decisions, B estimate	lead	lead	—
Platform / DevOps Engineer	Terraform modules, CI/CD templates, Argo CD, observability	●	●	—
Kubernetes Engineer	containerisation, Helm charts, cluster set-up, wave execution	part	●	—
Project Manager	plan, waves, cutover coordination	part	part	—
Platform Ops Lead	monthly operations, capacity, reporting	—	—	lead
Platform Engineer	operations, upgrades, incidents, small changes	—	—	●

● takes part lead accountable for delivery part part time — not staffed

CUSTOMER-SIDE CONTACTS «GÜNER DOĞRULASIN»

Application owners
inventory, interviews, decisions per application, go / no-go per wave

Test team
UAT and functional smoke tests are run by the customer

Network and security team
firewall, connectivity, identity, security approvals

Person dependency (S11).
Delivery capacity sits in the cloud team, not in the SAT data / AI core. People who delivered the Ecofin work: «NUMBER».

Staffing facts to collect.
Kubernetes engineers «NUMBER» · CKA / CKAD certified «NUMBER» · Terraform / Argo CD experience «NUMBER»

Sizing — Drivers, S / M / L Bands and Effort

draft — no recorded effort

KOMTAS

Drivers come from the input forms (files 3a–3c). Durations in working days or weeks, effort in person-days (pd), C in hours per month.

SIZING DRIVERS «GÜNER DOĞRULASIN»

DRIVER	S	M	L
Applications	≤10	11–30	>30
Share of complex applications	<20%	20–40%	>40%
Environments	≤2	3	>3
Target SLA	99.5%	99.9%	99.95%+ (multi-zone / region)

Band rule. «GÜNER DOĞRULASIN»
The band is the highest band reached by at least three of the four drivers. A driver at L also counts as reaching M and S. The band sets A duration and effort and the size of B Phase 1.

Example.
25 applications (M), 30% complex (M), 4 environments (L), 99.9% SLA (M) → four drivers at M or above, one at L → band M.

DURATION / EFFORT «GÜNER DOĞRULASIN»

ITEM	S	M	L
A duration	3 weeks	3.5 weeks	4 weeks
A effort	~20 pd	~25 pd	~30 pd
A customer effort	3 days	4 days	5 days
B Phase 1 «GÜNER DOĞRULASIN»	~30 pd	~35 pd	~40 pd
C capacity	40 h / month	80 h / month	160 h / month

B Migration not by band: Phase 3 from the A inventory (count per class × unit effort); the band sizes Phase 1 only. C band from cluster and application count.

Calibration.
Draft — no recorded effort. Bands and person-days are updated with Güner Hacıoğlu's data from the Ecofin work.

Acceptance Criteria

KOMTAS

Each application is accepted in the target on its own. Thresholds are set per customer; no figure is promised in advance.

ACCEPTANCE PER APPLICATION «GÜNER DOĞRULASIN»

1. **Test cases agreed**
   in the wave plan: smoke tests and performance scenarios per application
2. **Rollback plan tested**
   written and run in the test environment before cutover
3. **Cutover and checks**
   smoke test and performance run by the customer in the target
4. **Sign-off per application**
   application owner signs; open items go to hypercare or C

CRITERIA AND THRESHOLDS «GÜNER DOĞRULASIN»

CRITERION	CHECKED BY	MEASURE	THRESHOLD
Functional smoke test	customer	agreed test cases pass in the target	«NUMBER»%
Performance	customer + Komtaş	agreed scenarios; response time against the on-prem baseline	within «NUMBER»%
Rollback	Komtaş	rollback plan executed in test; time to roll back	≤ «NUMBER» min
Runs via GitOps	Komtaş	deployed by Argo CD from Git; no manual change in the cluster	yes / no
Observability	Komtaş	dashboards and alerts active for the application	yes / no

Thresholds per customer.
Thresholds are agreed in A or at the start of B on the customer's own scenarios. No figure is promised in advance.

Outside acceptance.
Functional defects that already exist on-prem, and the end-user testing itself (customer UAT), are not acceptance criteria of the migration.

Follow-on Map

KOMTAS

Each tier leads to a named next step. In the proposal templates this is the section 'Next step', without margin figures.

AFTER → NEXT STEP «GÜNER DOĞRULASIN»

AFTER	NEXT STEP	TYPE
A read-out	B Migration: platform foundation, pilot and waves	service project
B go-live	C Platform Ops: monthly operations	recurring service
More applications	additional waves on the same platform	service project
After go-live	Cloud Checkup: cost, access and configuration review	assessment
Data on the same estate	etl-migration-gcp, data-modernization	project
Overall	Google Cloud or Azure consumption through Komtaş	consumption

In the proposal templates.
Section 'Next step': follow-on project, operations, consumption. No margin figures, no prices.

Entry from Cloud Checkup.
Checkup findings can name applications to modernise; they feed the A inventory.

Risks and Open Points

KOMTAS

Known risks of the package as drafted, and the questions that stay open after the 15.10.2026 meeting.

RISKS

RISK	EFFECT	HANDLING
Single reference	weak evidence for sales; S1 risk	Ecofin case written up; second customer as pilot
Person dependency in the cloud team (S11)	delivery capacity limited to a few people	second team trained on the stack; shared Terraform and Helm modules
Hidden dependencies	waves slip; cutovers rolled back	dependency mapping in A; pilot first; reserve in the wave plan
Legacy runtimes	applications cannot run in containers	Rehost as interim step or Retain; recorded in A
Licences for containerised commercial software	vendor terms block the move	checked per application in A; Repurchase or Retain
Customer test capacity	UAT delays the waves	test owners named in the proposal; test windows in the wave plan

OPEN POINTS BY OWNER

Güner Hacıoğlu — delivery

- Ecofin: app count, cloud, duration, team
- Effort per application by class
- CI/CD and observability tools used
- Acceptance and rollback practice

Sales

- Modernization pipeline; second customer
- Day rates, unit prices, T&M cap
- Monthly fee for C
- Use of the Ecofin name

Management

- Cloud team delivery capacity (S11)
- Place outside the 360 layers
- First Azure delivery
- Boundary with the data packages

Verification Summary

KOMTAS

Draft for Güner Hacıoğlu's review. Every drafted statement carries the orange verification tag and has one question in the sidecar file.

04 · VERIFICATION

TAGS IN THIS FILE

43

tags, same in EN and TR

sidecar: app-modernization-1-blueprint-tr.json

full list: app-modernization-guner-dogrulama-listesi.xlsx

TAGS BY SECTION

Positioning and commercial logic	2 – 6	10
Method and architecture	7 – 12	10
Delivery	13 – 19	22
Follow-on and status	20 – 22	1

PACKAGE FILES

1	**Blueprint (this file)**	43
2	**Customer presentation**	29
3a–c	**Input forms**	52
4a–c	**Proposal templates**	137

Package total: 261 tags, same in EN and TR.
3a 14 · 3b 26 · 3c 12 · 4a 49 · 4b 43 · 4c 45

HOW THE REVIEW WORKS

1. Answer each question in the sidecar file
2. Confirmed: the tag is removed
3. Changed: text updated in EN and TR
4. Effort and bands recalibrated with real data

Known facts carry no tag: Ecofin — on-prem applications containerised and moved to cloud with Kubernetes, Terraform, Helm and Argo CD by the Komtaş cloud team; Google Cloud Premier partnership; completed Azure partnership.
