KOMTAS

DATA PLATFORM OPERATIONS SUPPORT

Blueprint v1 — internal reference, draft for Damalink and Digitallency

A Platform Health Check · B Transition · C Operate · modules Informatica, Teradata, BI, DWH · SLA and service catalogue

1 **Positioning and commercial logic**
Summary, commercial logic, evidence, target customers and triggers, scope, link to migrations, tiers.
p. 2 – 8

2 **Health Check and monitoring**
A flow and timeline, scoring, standards and control points, Monitoring Accelerator.
p. 9 – 12

3 **Transition and operations**
B Transition, C service models, modules, technology options, SLA and service catalogue.
p. 13 – 18

4 **Delivery and status**
Team, sizing, acceptance, accelerators, follow-on, risks, verification summary.
p. 19 – 25

Package Summary — What, for Whom, When

KOMTAS

Operations support for DWH, ETL and BI environments: platform health check, monitoring, incident, change, performance and capacity management, expert resource model.

01 · SUMMARY

WHAT THE PACKAGE DELIVERS

Inventory and health score
environments, jobs, reports, users; score per module

Standards and monitoring results
repository queries, control points, rule scan

Managed transition
knowledge transfer, runbooks, shadow, handover

Operations under SLA
incident, change, performance, capacity

Expert resource model
hour pool, dedicated FTE or hybrid

THREE TIERS «DIGITALLENCY DOĞRULASIN»

A — Platform Health Check

inventory, standards, performance, monitoring scan, score, operating model proposal

3–6 weeks, fixed fee

B — Transition

knowledge transfer, runbooks, monitoring set-up, SLA baseline, shadow

one-time, fixed fee

C — Operate

package, dedicated or hybrid; modules Informatica, Teradata, BI, DWH

monthly, min. 12 months

BASIS — KNOWN FACTS

- Damalink 04 Data Integration Framework: Data Integration Assessment and PowerCenter Monitoring Accelerator
- Damalink material dated 2019–2021; on-prem PowerCenter 10.x
- Digitallency deck: THY, Şişecam, Vodafone, SABB, Bank of Mısr and STC-KSA operations references
- Digitallency Resourcing Hub: DWH / BI developer, data modeller, architect, analyst; Teradata outsourcing
- Demand signals: Allianz ADM managed services, Digiturk resource model, Odeabank server move
- Partnership models with Damalink and Digitallency not yet settled

Status: draft v1. Built from the Damalink framework material and the Digitallency references. Method, rules, durations, efforts, bands, SLA items, roles and acceptance criteria carry an orange tag naming the owner who verifies them (p. 25).

Commercial Logic — Partnerships Open

internal only

KOMTAS

Internal only. Partner terms, references by name and the demand signals never appear in the customer deck or in the proposal templates.

PARTNERSHIP WITH DAMALINK · OPEN «DAMALINK DOĞRULASIN»

ITEM	STATUS
Delivery capacity	«FIELD»
Use of method, queries, checklists	«FIELD»
Monitoring Accelerator use	«FIELD»
Revenue share	«FIELD»
Proposal lead	«FIELD»

Digitallency. «DIGITALLENCY DOĞRULASIN»
Use of the operations references and the Resourcing Hub roles in Komtaş proposals and delivery: «FIELD». Until agreed, customer files use anonymous wording only.

WHERE THE VALUE IS

A Platform Health Check
fixed fee; inventory, score, operating model

↓

B Transition
one-time; runbooks, monitoring, shadow

↓

C Operate
monthly, recurring; account anchor

↓

Migrations
etl-migration-gcp; PowerCenter → IDMC

Demand signals. RFP folder: Allianz Data Office ADM managed services specification; Digiturk senior resource model; Odeabank Informatica server move. Not references.

COMMERCIAL POINTS

1. Recurring revenue; the C contract anchors the account
2. Health Check inventory feeds legacy ETL → GCP and PowerCenter → IDMC (licence / IPU)
3. Several package Run tiers (Predictive, Data Privacy, MDM…) consolidated in one C contract
4. Gulf references (SABB, Bank of Mısr, STC) support a regional narrative
5. Pricing structure of each service model «FIELD»

Gulf narrative. Teradata consultancy support for two banks in the Gulf region and Egypt and outsourced consulting in Saudi Arabia give a regional story for operations support. Use of these references is agreed with Digitallency first.

Evidence and Sources

KOMTAS

What the package rests on today. Internal only: partners and references are named here; customer files use anonymous references.

01 · EVIDENCE

SOURCES

37 rules

Damalink — 04 Data Integration Framework
«DAMALINK DOĞRULASIN»

Data Integration Assessment: seven scored categories, operational and governance repository queries, performance control points, deployment checklist, questionnaires. PowerCenter Monitoring Accelerator: 37 rules, data model, dashboards, alerts.

6 references

Digitallency — operations references
«DIGITALLENCY DOĞRULASIN»

THY DWH & BI operation support; Şişecam BI support; Vodafone Informatica support; SABB and Bank of Mısr Teradata consultancy support; STC-KSA outsourced consulting; Resourcing Hub roles.

SOURCE STATUS

Damalink — assessment method approach, scoring, queries, checklists	source
Damalink — Monitoring Accelerator 37 rules, data model, approach	source
Digitallency — operations references six references, Resourcing Hub	source
Content dates 2019–2021; on-prem PowerCenter 10.x	to confirm
Use in Komtaş proposals permission; partner or Komtaş reference	to confirm
Komtaş own reference «REFERENCE PROJECT»	no reference

Reference years, scope and results: not in the deck «RESULT».
«DIGITALLENCY DOĞRULASIN»

GAPS AND OPPORTUNITY

Old material

Damalink content dates from 2019–2021 and covers on-prem PowerCenter 10.x only; IDMC equivalents are drafted (p. 16).

Partner IP and references

Use of the Damalink queries, checklists and Monitoring Accelerator, and of the Digitallency references, in Komtaş proposals is open.

Door to migrations

The Health Check inventory is the input to etl-migration-gcp and to PowerCenter → IDMC migration (p. 7).

Customer naming. Customer files use: an airline — DWH & BI operations support; a manufacturing group — BI support; a telecom operator — Informatica support; two banks in the Gulf region and Egypt — Teradata consultancy support; a telecom operator in Saudi Arabia — outsourced consulting.

Target Customers and Triggers

KOMTAS

Who is approached and the situations that start the conversation. Drafted from the references and the demand signals.

TARGET CUSTOMER PROFILES «DIGITALLENCY DOĞRULASIN»

Banks and insurance
large DWH, regulatory loads

Telecom
high volumes, many ETL jobs

Airlines and manufacturing
DWH and BI used every day

Gulf region
Teradata and outsourced support

TRIGGERS «DIGITALLENCY DOĞRULASIN»

Vendor contract ending
the current support contract ends or is retendered.

Key staff leaving
platform knowledge held by one or two people.

Failed jobs
frequent job failures, manual restarts.

Missed load windows
reports reach business users late.

Audit findings
findings on operations, access or change control.

Platform end of life
version out of support; upgrade or move needed.

Cost pressure
in-house team or vendor cost under review.

Planned migration
the old platform must run stably until cut-over.

First call. Platforms and versions, environments, number of jobs and reports, current team or vendor and contract end, incident history, support window needed, planned migration. The answers feed the input form (file 3a).

Scope Boundary — What It Is Not

KOMTAS

What the package does not do, and the Komtaş packages it links to without absorbing them.

01 · BOUNDARY

OUT OF SCOPE «DIGITALLENCY DOĞRULASIN»

- Infrastructure and hardware operations
- Operating system and database administration (DBA)
- Network
- Licence management
- New development beyond the minor enhancement pool

BOUNDARY TO DWH ASSESSMENT



DWH Assessment looks at the target; the Health Check looks at the run.

dwh-assessment reviews architecture and target state. The Health Check is operational: jobs, schedules, performance, monitoring, standards and deployment. Both can run on the same platform; findings are shared, not repeated.

RELATED PACKAGES



etl-migration-gcp / IDMC the Health Check inventory is the migration input (p. 7).



Package Run tiers Predictive, Data Privacy, MDM, Regulatory Reporting, Datamart Run tiers can move under C.



dwh-assessment architecture and target state of the warehouse.

Boundary rule. Infrastructure, OS, DBA, network and licences: customer or its providers; optional lines possible. Architecture and target state: dwh-assessment. Moving off the platform: migration packages. Running the platform under SLA: this package.

Link to Migrations — etl-migration-gcp and PowerCenter → IDMC

KOMTAS

The Health Check inventory and findings are inputs to a migration; C Operate can run the old platform while it moves.

HEALTH CHECK → MIGRATION «DAMALINK DOĞRULASIN»

HEALTH CHECK OUTPUT	CONTENT	USE IN MIGRATION
Inventory	workflows, sessions, mappings, jobs, schedules, reports	scope and wave plan for legacy ETL → GCP or IDMC
Standards findings	invalid, unused and duplicate objects	what is migrated, cleaned or retired
Performance findings	busy %, SQL overrides, pushdown use	design points for the target platform
Dependencies	schedules, load chains, sources and targets	cut-over order
Monitoring rules	rule set and thresholds	same checks rebuilt on the target
Run during migration	C Operate on the old platform	stable run until cut-over; parallel run
Licence view	PowerCenter use per environment	IDMC licence and IPU sizing input

Run while moving.
During a migration the old platform keeps running. C Operate covers it until cut-over and is reduced module by module; the migration team has one source of operational knowledge.

IDMC sizing. «DAMALINK DOĞRULASIN»
IPU sizing for IDMC needs the inventory counts and run times from P1. PowerCenter → IDMC conversion tooling and terms «FIELD».

Tiers — Health Check, Transition, Operate

KOMTAS

A finds out what is there and proposes the operating model; B takes the operation over; C runs it every month.

01 · TIERS

A — Platform Health Check

fixed fee by band

«DAMALINK DOĞRULASIN»

- kick-off, access, module scope
- inventory and questionnaire
- standards, performance, monitoring scan
- health score in seven categories
- operating model proposal, B and C estimate

S 3 · M 4 · L 6 weeks

B — Transition

fixed fee, one-time

«DIGITALLENCY DOĞRULASIN»

- knowledge transfer from the current team
- runbooks and operations documents
- monitoring set-up, SLA baseline
- ticket flow, priority, escalation
- shadow, reverse shadow, handover

S ~15 · M ~30 · L ~50 pd + shadow

C — Operate

monthly

«DIGITALLENCY DOĞRULASIN»

- package: SLA + ticket or hour pool
- dedicated: FTE experts in the team
- hybrid: core FTE + SLA pool
- incident, change, performance, capacity
- monthly SLA report

minimum 12 months (draft)

MODULES — CHOSEN IN A SCOPE AND IN C

Informatica | Teradata | BI | DWH

Entry point. Most customers start with A. A customer with documented operations can start with B on an equivalent inventory. C is not offered without the monitoring baseline from A or B.


A — Platform Health Check: Flow and Timeline

KOMTAS

Kick-off, investigate, assess, report and propose the operating model in phases P0–P4. Fixed fee by band.

02 · TIER A

PLAN · BAND M, 4 WEEKS

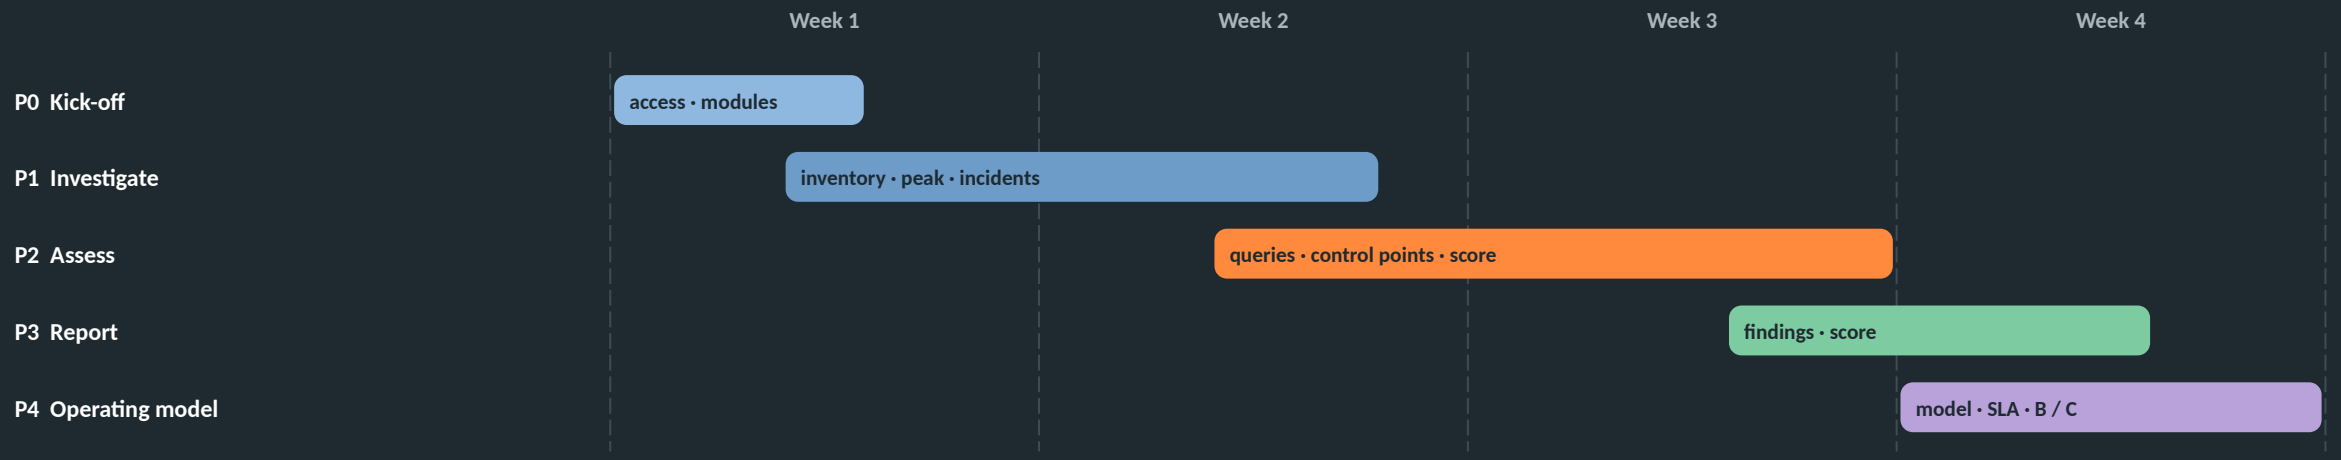

Band S 3 weeks / ~15 pd, band M 4 weeks / ~25 pd, band L 6 weeks / ~40 pd. Damalink reference for a full assessment: 1–2 months. «DAMALINK DOĞRULASIN»

DECISION FOR B AND C

Operating model and B / C estimate

The report names the service model, modules, SLA proposal, support window, team and transition plan, with the B and C estimate and a migration readiness note. The customer decides.

DELIVERABLES «DAMALINK DOĞRULASIN»

- Requirement document
- Inventory
- Findings list
- Health score
- Standards and monitoring results
- Operating model proposal

Precondition. Read-only access to repositories, logs and schedules, or agreed query outputs run by the customer. Without either, A is blocked.

Health Check Scoring — Seven Categories

KOMTAS

Questions answered 0–5 per category and weighted to a score out of 5 per module. Pattern from the Damalink assessment, extended to all modules.

CATEGORIES AND WEIGHTS «DAMALINK DOĞRULASIN»

CATEGORY	WEIGHT	WHAT IS CHECKED
Architecture	10%	environments, HA / DR, resources, versions
Development	20%	reuse, team development, versioning
Standards	20%	naming, parameters, descriptions, hard-coding
Deployment	10%	promotion method, pre-checks, rollback
Performance	10%	bottlenecks, pushdown, caches, long runs
Stability & maintenance	20%	peak load, failed and zombie jobs, disk, logs
Security & user management	10%	LDAP, groups, roles, shared and admin users

Weighted score.
Σ (category average × weight) on the 0–5 scale; one score per module. Each finding carries criticality and a recommendation; quick wins are listed separately.

Evidence per answer.
Interviews and questionnaire, repository queries, session logs, schedules and incident history. Each answer records its source; statements without evidence are marked.

0–5 SCALE «DAMALINK DOĞRULASIN»

- **0** not in place
- **1** ad hoc, depends on individuals
- **2** partly defined
- **3** defined, not checked
- **4** defined and checked
- **5** checked automatically

Extension to Teradata, BI, DWH. «DIGITALLENCY DOĞRULASIN»
Same seven categories; questions rewritten per module (e.g. workload rules for Teradata, refresh and gateways for BI). Weights per module «FIELD».

Standards, Performance Control Points, Deployment Checklist

KOMTAS

Read-only checks run in P2. Results go to the findings list and the score; the same checks feed monitoring in C.

02 · TIER A

Standards queries

operational ~25 · governance ~30

«DAMALINK DOĞRULASIN»

- invalid or unused objects
- zombie workflows, zero-row runs
- rejected rows above threshold
- oversized workflows and mappings
- hard-coded paths, pre / post SQL
- naming by object type
- descriptions, shortcuts, parameters

repository queries + command line

Performance control points

from session logs and settings

«DAMALINK DOĞRULASIN»

- source / target / transformation busy %
- commit interval, bulk or normal load
- SQL override, source filter
- lookup, joiner, aggregator caches
- sorter temp I/O, sequence cache
- pushdown, DTM buffer, partitioning

session log parser

Deployment checklist

before promotion to production

«DAMALINK DOĞRULASIN»

- mapping development checks
- transformation checks by type
- workflow and session settings
- developer unit test evidence
- deployment group or export / import
- rollback method

automated where possible

Beyond Informatica. For the Teradata, BI and DWH modules the same three checks are written per platform in A, e.g. skew and statistics, refresh failures, load chain gaps. «DIGITALLENCY DOĞRULASIN»

PowerCenter Monitoring Accelerator

KOMTAS

Rule-based monitoring on the PowerCenter repository: pre-defined, extendable rules with weights, thresholds and owners. Set up in B, run in C.

02 · MONITORING

WHAT IT DETECTS «DAMALINK DOĞRULASIN»

Failed runs
workflows and sessions

Rejected records
above the threshold

Run-time deviation
longer or shorter than average

Row-count deviation
more or fewer rows than average

Zombie and zero-row runs
stuck runs, empty completions

Standards breaches
naming, invalid objects

Design risks
SQL overrides, pushdown use

APPROACH «DAMALINK DOĞRULASIN»

1 **Define**
metrics, categories, weights, thresholds, owners, new rule queries

2 **Measure**
run the queries, drill down to objects, track several metrics

3 **Manage**
schedule, report, alert, keep logs and privileges, add rules

CONTENT

37 rules, two families «DAMALINK DOĞRULASIN»

Operational: performance and maintenance. Governance: performance, maintenance, standards. Each rule: category, critical flag, weight, threshold, schedule, e-mail.

Dashboards and alerts

Health by category, drill-down to the faulty object, e-mail alerts for critical rules, logs and user privileges.

IDMC equivalent «DAMALINK DOĞRULASIN»

On-prem PowerCenter only. On IDMC: Operational Insights and native monitoring «FIELD».

Partner IP. Damalink IP; usage terms in Komtaş contracts «FIELD». Without agreement, the checks are rebuilt as Komtaş queries. «DAMALINK DOĞRULASIN»

B — Transition

fixed fee, one-time

KOMTAS

Taking operations over from the current team or vendor. Accepted with the handover sign-off after the shadow period.

Prerequisite: a Platform Health Check or an equivalent inventory «A REF».

WORKSTREAMS «DIGITALLENCY DOĞRULASIN»

- **Knowledge transfer** — sessions with the current team or vendor
- **Runbooks** — operations documents per module
- **Monitoring set-up** — rules, alerts; Accelerator if Informatica
- **SLA baseline** — measured before targets are fixed
- **Ticket flow** — priority and escalation matrices
- **Access and tooling** — accounts, VPN, ticket tool, logs

EFFORT FORMULA «DIGITALLENCY DOĞRULASIN»

B EFFORT (pd)

workstreams by band + shadow period + optional line

WORKSTREAMS BY BAND

S ~15 pd · M ~30 pd · L ~50 pd

SHADOW

«NUMBER» weeks shadow, then reverse shadow

Optional line «OPTIONAL». «DAMALINK DOĞRULASIN»
Platform move or upgrade, e.g. an Informatica server move or a version upgrade (Odeabank-type demand).

TRANSITION PHASES «DIGITALLENCY DOĞRULASIN»

PHASE	CONTENT	EXIT	RUNS
Prepare	access, tools, plan	access granted	both
Knowledge transfer	sessions, runbooks	runbooks reviewed	current
Shadow	current team runs, Komtaş watches	«NUMBER» weeks	current
Reverse shadow	Komtaş runs, current team watches	no open P1	Komtaş
Handover	sign-off; SLA starts	signed	Komtaş

Shadow length depends on documentation level and number of modules.

C — Operate: Three Service Models

KOMTAS

Monthly operations under SLA. The model is proposed in A and chosen in the proposal; modules are added within the model.

03 · TIER C

«MODEL — PACKAGE»

SLA + monthly ticket or hour pool

«DIGITALLENCY DOĞRULASIN»

- services from the SLA catalogue
- pool S 80 · M 160 · L 320 h / month
- unused hours not carried over
- priority matrix P1–P4
- monthly SLA report

pricing structure «FIELD»

«MODEL — DEDICATED»

FTE experts in the customer team

«DIGITALLENCY DOĞRULASIN»

- roles from the FTE list (p. 19)
- seniority levels
- replacement and continuity rules
- customer directs daily work
- Digiturk-type demand

pricing structure «FIELD»

«MODEL — HYBRID»

core FTE + SLA pool

«DIGITALLENCY DOĞRULASIN»

- core FTE for the daily run
- pool for peaks and other modules
- one service manager
- SLA on pool services
- one monthly report

pricing structure «FIELD»

Term. Draft minimum term 12 months. Unused pool hours are not carried over; work above the pool is charged at the hour rate «FIELD». «DIGITALLENCY DOĞRULASIN»

Modules — Informatica, Teradata, BI, DWH

KOMTAS

Chosen in A scope and in C. Each module has its own lead, checks and runbooks.

«MODULE — INFORMATICA»
«DAMALINK DOĞRULASIN»

- PowerCenter and IDMC operations
- Monitoring Accelerator
- standards and deployment checks
- upgrades and patches support
- server move «OPTIONAL»

Damalink method

«MODULE — TERADATA»
«DIGITALLENCY DOĞRULASIN»

- workload management
- performance tuning
- space and capacity
- statistics
- backup coordination

Gulf references

«MODULE — BI»
«DIGITALLENCY DOĞRULASIN»

- Power BI, Qlik, SAP BusinessObjects
- report failures, refresh schedules
- gateways, users, authorisation
- universe / semantic model changes
- report performance

airline, manufacturing

«MODULE — DWH»
«DIGITALLENCY DOĞRULASIN»

- load chain monitoring
- data model changes
- data quality checks
- Oracle, SQL Server
- cloud warehouses

platform list «PLATFORM»

WHAT EACH TIER DOES PER MODULE «DIGITALLENCY DOĞRULASIN»

TIER	INFORMATICA	TERADATA	BI	DWH
A	standards queries, checklist, rule scan	workload, skew, space, statistics review	refresh failures, gateways, usage review	load chain, model, DQ check review
B	Accelerator set-up, runbooks	workload and space runbooks	refresh and gateway runbooks	load chain runbooks
C	failures, deployments, upgrades	tuning, capacity, statistics	failures, refresh, users, changes	loads, model changes, DQ

Modules not chosen in A can be added in C after a short module health check.

Technology Options — On-premises and Cloud

KOMTAS

The Damalink material covers on-prem PowerCenter 10.x. IDMC and cloud equivalents are drafted and must be confirmed. The platform list is a scope item «PLATFORM».

PLATFORMS BY NEED «DAMALINK DOĞRULASIN»

NEED	ON-PREMISES	CLOUD / IDMC
Data integration	Informatica PowerCenter	IDMC Cloud Data Integration
Monitoring	repository queries; Monitoring Accelerator	IDMC Operational Insights «FIELD»
Deployment	deployment groups, command-line utilities	IDMC asset export / import «FIELD»
Data warehouse	Teradata, Oracle, SQL Server	cloud warehouses, e.g. BigQuery «PLATFORM»
BI	Power BI Report Server, Qlik Sense, SAP BusinessObjects	Power BI service, Qlik Cloud «PLATFORM»

Choice per customer «PLATFORM».
The platform list is fixed in A scope. PowerCenter and IDMC can run side by side during a migration; C covers both.

Support status. «DAMALINK DOĞRULASIN»
Support status of PowerCenter 10.x and the IDMC monitoring scope «FIELD»; checked with Informatica before each proposal.

SLA and Service Catalogue — Services

KOMTAS

Five core services and three optional ones. Each service has a definition and scope, trigger, output and measure.

SERVICE CATALOGUE «DIGITALLENCY DOĞRULASIN»

SERVICE	DEFINITION AND SCOPE	TRIGGER	OUTPUT	MEASURE
Incident management	restore failed jobs, loads and reports; workaround, root cause note	alert or ticket	restored run, incident record	response and resolution by priority
Change & minor enhancement	small changes from the pool: mappings, reports, schedules	change request	tested change, deployment	delivered on the agreed date
Performance management	long-running jobs and slow reports analysed and tuned	threshold or request	tuning, before / after times	run-time trend
Capacity management	space, CPU, licence and load-window headroom tracked	monthly review, threshold	capacity note, actions	headroom against threshold
Reporting	monthly SLA report, trends, improvement backlog	month end	SLA report	on time, accepted
Problem mgmt. «OPTIONAL»	recurring incidents traced to root cause	repeated incident	problem record, fix	repeat incidents
Release support «OPTIONAL»	release and deployment to production with checks	release plan	deployed release, checklist	failed deployments
On-call «OPTIONAL»	response outside the support window	P1 / P2 out of hours	incident record	on-call response

Per service.
Each service is written in the proposal annex with definition, scope, trigger, output and measure; targets are agreed after the SLA baseline in B.

Not in the catalogue.
Infrastructure, OS, DBA, network and licence work; new development beyond the minor enhancement pool.

SLA and Service Catalogue — Priorities, Windows, Escalation

KOMTAS

Targets stay placeholders until the SLA baseline is measured. Service credits and their structure are agreed per contract.

PRIORITY MATRIX «DIGITALLENCY DOĞRULASIN»

PRIORITY	DEFINITION	EXAMPLE	RESPONSE	RESOLUTION
P1	critical load or report down; business stopped	month-end or regulatory load failed	«NUMBER» h	«NUMBER» h
P2	major function degraded; workaround hard	daily DWH load late	«NUMBER» h	«NUMBER» h
P3	limited impact; workaround exists	one report failing	«NUMBER» h	«NUMBER» days
P4	request or question	new user, minor change	«NUMBER» days	as planned

SUPPORT WINDOWS «DIGITALLENCY DOĞRULASIN»

8×5 business hours, working days

12×5 extended hours «OPTIONAL»

24×7 on-call for P1 / P2 «OPTIONAL»

ESCALATION LEVELS «DIGITALLENCY DOĞRULASIN»

1. **Operator** ticket owner
2. **Module lead** technical escalation
3. **Service manager** SLA and customer contact
4. **Steering** platform owner and Komtaş management

CREDITS AND REPORTING

Service credits «FIELD».
Structure and caps agreed per contract.

Monthly SLA report.
tickets by priority, targets met, trends, capacity, backlog

Team and Roles

KOMTAS

A service manager runs the service with module leads and operators / developers; the dedicated model adds FTE roles embedded in the customer team.

ROLES «DIGITALLENCY DOĞRULASIN»

ROLE	RESPONSIBILITY	A	B	C
Service manager	SLA, monthly report, escalation, customer contacts	lead	lead	lead
Health check lead	method, interviews, score, operating model proposal	●	part	—
Module leads	Informatica, Teradata, BI, DWH checks and runbooks	●	●	●
Operators / developers	incidents, changes, monitoring, minor enhancements	part	●	●
Dedicated FTE	roles below, embedded in the customer team	—	part	●

● takes part lead accountable for delivery part part time — not staffed

CUSTOMER-SIDE CONTACTS «DIGITALLENCY DOĞRULASIN»

Platform owner
service owner, sign-off

Business owners
priorities, report users

Infrastructure / DBA
servers, databases, access

Security
accounts, approvals, audit

Dedicated FTE roles. «DIGITALLENCY DOĞRULASIN»
DWH / BI developer · ETL developer · data modeller · architect · analyst · Teradata expert · Informatica administrator. Seniority levels, replacement and continuity rules «FIELD».

Staffing facts to collect.
Available FTE by role «NUMBER» · partner share «FIELD» · on-site or remote «FIELD»

Sizing — Drivers, Bands and Effort

draft — to calibrate

KOMTAS

Drivers come from the input forms (files 3a–3c). Durations in weeks, effort in person-days (pd), pools in hours per month.

SIZING DRIVERS «DIGITALLENCY DOĞRULASIN»

DRIVER	S	M	L
Modules	1	2	≥3
Jobs / workflows	≤300	301–1,500	>1,500
Reports / BI users	≤100 / ≤200	101–500 / 201–1,000	>500 / >1,000
Environments	1–2	3	≥4
Support window	8×5	12×5	24×7
Monthly tickets (avg.)	≤40	41–150	>150

Band rule. «DIGITALLENCY DOĞRULASIN»
The band is the highest band reached by at least three drivers. The dedicated model is sized in FTE, not in bands.

Dedicated and hybrid. «DIGITALLENCY DOĞRULASIN»
FTE count by role from input form 3c; hybrid = core FTE + pool band. The 3c capacity calculator gives pool hours by band and module.

DURATION / EFFORT «DIGITALLENCY DOĞRULASIN»

ITEM	S	M	L
A duration	3 weeks	4 weeks	6 weeks
A effort	~15 pd	~25 pd	~40 pd
B effort	~15 pd	~30 pd	~50 pd
B shadow	«NUMBER» weeks	«NUMBER» weeks	«NUMBER» weeks
C package pool	80 h / month	160 h / month	320 h / month
C dedicated	«NUMBER» FTE	«NUMBER» FTE	«NUMBER» FTE
C hybrid	FTE + pool	FTE + pool	FTE + pool

Modules Modules count as a driver; fees «...». «DIGITALLENCY DOĞRULASIN»

Calibration.
Draft. A calibrated to the Damalink assessment duration; B and C to be calibrated with Digitallency's operations contracts.

Acceptance Criteria

KOMTAS

Each tier is accepted on agreed evidence. SLA targets are fixed after the baseline; none is promised in advance.

ACCEPTANCE STEPS

1. **Criteria agreed**
   per tier, at start, with the platform owner
2. **Evidence collected**
   report, runbooks, sign-off sheet, SLA report
3. **Review**
   open points fixed or explained
4. **Sign-off**
   platform owner

CRITERIA «DIGITALLENCY DOĞRULASIN»

TIER / ITEM	CRITERION	EVIDENCE	THRESHOLD
A	Health Check report accepted	report, read-out	accepted at read-out
B runbooks	runbooks per module reviewed	runbook set	all modules in scope
B baseline	SLA baseline measured	baseline report	«NUMBER» weeks of data
B handover	handover after reverse shadow	sign-off sheet	no open P1
C monthly	monthly SLA report accepted	SLA report	each month
C credits	service credits applied as agreed	SLA report	«FIELD»

Targets after the baseline.
Response and resolution targets are fixed after the SLA baseline in B; none is promised before.

Outside acceptance.
Failures caused by infrastructure, source systems or out-of-scope platforms are recorded but not counted against the SLA.

Accelerators

KOMTAS

Six reusable assets. 1–5 come from the Damalink framework and are rewritten in Komtaş structure; 6 is a set of Komtaş templates.

03 · ACCELERATORS

1 Health Check scoring model

«DAMALINK DOĞRULASIN»

Seven weighted categories, 0–5 questions, weighted score per module.

architecture · development · standards · deployment · performance · stability · security

Damalink pattern; extension new — A

2 Standards queries and deployment checklist

«DAMALINK DOĞRULASIN»

Operational and governance repository queries; checks before promotion.

~25 operational · ~30 governance queries · checklist by object

Damalink query set — A · B

3 Performance control points

«DAMALINK DOĞRULASIN»

Checks and thresholds read from session logs and settings.

busy % · caches · commit · pushdown · buffers · log parser

Damalink control points — A · C

4 PowerCenter Monitoring Accelerator

«DAMALINK DOĞRULASIN»

37 rules with weights, thresholds, alerts and dashboards on the repository.

operational and governance rules · drill-down · e-mail alerts

Damalink IP; terms «FIELD» — B · C

5 Questionnaires

«DAMALINK DOĞRULASIN»

Requirement and developer / operator questions for A interviews and the input forms.

architecture · stability · performance · deployment · security · alerts

rewritten from Damalink — A

6 Runbook, SLA and report templates

«DIGITALLENCY DOĞRULASIN»

Runbook per module, transition plan, SLA catalogue and monthly report.

runbooks · transition plan · SLA catalogue · monthly report

Komtaş templates — B · C

Rewritten, not copied. All six are adapted to Komtaş structure and language. Use of the Damalink originals in proposals is agreed before they are named.

Follow-on Map

KOMTAS

Each tier leads to a named next step. In the proposal templates this is the section 'Next step', without partner terms.

AFTER → NEXT STEP «DIGITALLENCY DOĞRULASIN»

AFTER	NEXT STEP	TYPE
A report	B Transition, then C Operate	service project
A inventory, migration planned	etl-migration-gcp (legacy ETL → GCP)	package
PowerCenter out of support or licence review	PowerCenter → IDMC migration; licence / IPU	project + licence
C running	more modules or another model (pool → hybrid)	recurring service
Several package Run tiers	consolidated under C	recurring service
Architecture questions	dwh-assessment	package
Standards and ownership findings	data-governance	package
Customer in the Gulf region	regional operations offer with Digitallency «FIELD»	programme

In the proposal templates.
Section 'Next step': migration readiness (etl-migration-gcp, IDMC), more modules, consolidation of Run tiers. No partner terms, no prices.

Recurring value.
C anchors the account; the inventory and the run knowledge position Komtaş for the migration.

Risks and Open Points

KOMTAS

Known risks of the package as drafted, how they are handled, and the questions still open.

RISKS «DIGITALLENCY DOĞRULASIN»

RISK	EFFECT	HANDLING
Undocumented environments	long knowledge transfer; hidden jobs	inventory in A; runbooks in B; shadow length by documentation
Knowledge held by few people	gaps at takeover	knowledge transfer plan per role; reverse shadow
Access and security approvals	late start, blocked checks	access list in P0; customer-run queries as fallback
SLA without monitoring baseline	targets missed from day one	baseline in B; targets fixed after the baseline
Partner IP terms	Accelerator or queries not usable	agree terms; rebuild as Komtaş queries if needed
Old references	references dated or not usable	Digitallency confirms years and permission

OPEN POINTS BY OWNER

Damalink

- Method current; IDMC equivalents?
- Monitoring Accelerator terms
- Assessment duration and effort
- Informatica delivery capacity

Digitallency

- References: years, scope, permission
- SLA and service-level practice
- Resourcing Hub roles, FTE model
- Teradata / BI / DWH capacity

Sales and management

- Partnership models
- Pricing structure per model
- Demand signals follow-up
- Gulf region approach

Verification Summary

KOMTAS

Draft for review by Damalink and Digitallency. Every drafted statement carries an orange tag naming its owner and has one question in the sidecar file.

04 · VERIFICATION

TAGS IN THIS FILE

64

tags, same sequence in EN and TR

DAMALINK 26 DIGITALLENCY 38

sidecar: data-platform-ops-1-blueprint-tr.json

TAGS BY SECTION

Positioning, tiers	2 – 8	14
Health Check, monitoring	9 – 12	14
Transition, operations	13 – 18	19
Delivery, status	19 – 25	17

PACKAGE FILES

		TAGS
1	Blueprint (this file)	64
2	Customer deck	«...»
3a–c	Input forms	«...»
4a–c	Proposal templates	«...»

Package total: «...» tags; same in EN and TR.
One sidecar file per document; one question per tag; owner per tag.

HOW THE REVIEW WORKS

1. Each owner answers its questions in the sidecar
2. Confirmed: tag removed; changed: EN and TR updated
3. Placeholders filled: «FIELD», «NUMBER», «PLATFORM»
4. Durations, efforts, pools, SLA targets and IDMC names recalibrated

Known facts carry no tag: the structure and dates of the Damalink framework material, the references as named in the Digitallency deck, the demand signals in the RFP folder; partnership models open.
