KOMTAS

DATA GOVERNANCE PROGRAM

Blueprint — internal reference

Strategy & Framework · Technology Enablement · Managed Service · 10-category maturity model

1 **Positioning and market**
What is formalised, the 360 view, the source proposals as evidence, adjacent services. p. 2 – 6

2 **Method**
The 10-category maturity model, three pillars, operating model and the six standard processes. p. 7 – 13

3 **Tiers**
A Strategy & Framework, B Technology Enablement (modules, platform blocks, variants), C Managed Service. p. 14 – 22

4 **Delivery economics and package status**
Bands S / M / L calibrated on proposals, team, fee references, payment patterns, files, open items. p. 23 – 28

SECTION 1

Positioning and Market

What the package formalises, where it sits in the 360 architecture, the eight source proposals and the adjacent services.

What this package is — formalising a de facto template p. 3

Where this programme sits — AI value proposition p. 4

Market and evidence — eight customers, one shape p. 5

Scope boundary and adjacent services p. 6

What This Package Is — Formalising a De Facto Template

KOMTAS

Komtaş has sent the same data governance proposal to eight customers between July and October 2026. The structure was never written down as a package; this blueprint does that.

01 · WHAT THIS IS

WHAT EXISTS TODAY

One skeleton, reused

phased programme, 10-category assessment, Informatica implementation, MSU-based managed service

Shared text

paragraph overlap: OYAK to Aras 66%, Havelsan to Aras 56%, Havelsan to OYAK 53% (SAT text comparison)

Variants grew per deal

strategy only, rollout of an installed tool, migration to IDMC, catalogue and lineage only

Not yet a package

no bands, no recorded actual effort, no template; licence text mixed into service proposals

WHAT THE PACKAGE FIXES

A — Strategy & Framework

product-independent; maturity, organisation, policies, templates, pilot, roadmap

B — Technology Enablement

Informatica; modules B1 glossary, B2 catalogue and lineage, B3 data quality

C — Managed Service

optional; 12 months, monthly MSU capacity, service catalogue, SLA

DECISIONS (APPROVED)

- 10 maturity categories exactly as in the source
- Licences are a separate proposal, not in the templates
- Platform as two blocks: IDMC or on-prem; unused one deleted
- B priced module by module (B1 / B2 / B3)
- Migration and Rollout as B variants, not separate files
- Operational Data Governance stays a separate package

Why phases. Technology is a decision taken after the target model, not an assumption made before it: ownership, responsibilities and priority needs are set first, then the platform is configured to support them. The customer keeps control of the scope and timing of the technology investment.

Where This Programme Sits — AI Value Proposition

KOMTAS

Four layers. Each layer consumes the one below. This programme governs the Data / Analytic 360 foundation and supplies the meaning, ownership and quality signals the upper layers rely on.

Action 360

Intelligent Work Experience

Teams · Slack · WhatsApp · Web / Portal · Claude Desktop · API, Headless

Agent 360

Governed Digital Workforce

INDUSTRY: Manufacturing · Retail · Banking · Energy · Aviation · Other

FUNCTION: Customer Service · Sales · Finance · Procurement · Operations · Other

Context 360

Enterprise Context

Semantic Layer · Ontology · Knowledge Graph · Master Data · Corporate Memory

Data / Analytic 360

Trusted Data Foundation

THIS PROGRAMME · ACROSS THE FOUNDATION

Datawarehouse · Lakehouse · Integration · BI · **Governance / MDM**

AI-ready governance · glossary, ownership, classification, lineage and DQ scores that agents and models can read

No autonomous decision without trusted data: meaning, owner and quality of the data are known before agents act on it.

RELATION TO NEIGHBOURING LAYERS

Home: Governance / MDM

Glossary, catalogue, lineage, classification and data quality across warehouse, lakehouse, BI and source databases. Master and reference data is assessed (category 6); full MDM is a separate project.

Relation to Context 360

Business terms, metrics and ownership are the first input of the semantic layer, ontology and knowledge graph: one approved meaning per term.

Relation to Agent 360 and Action 360

The framework is built to extend to AI governance: model ownership, purpose, input data and policy links. On IDMC, governed metadata is reachable for agents through CLAIRE and MCP.

Market and Evidence — Eight Customers, One Shape

KOMTAS

The source proposals and the Penti customer deck. Internal file: customer names are used here and only here.

SOURCE PROPOSALS · JULY – OCTOBER 2026

CUSTOMER / DOCUMENT	DATE	SECTOR	SHAPE	DURATION IN PROPOSAL	PLATFORM
Aras Kargo — technical	02.10.2026	Logistics	full programme, 3 phases (main template)	A 6 wk · B 8 wk · C 12 mo	IDMC
Aras Kargo — commercial	06.10.2026	Logistics	same scope as Modules 1–5	M1 4 · M2 4 · M3 7 · M4 8 wk	IDMC
Aras Kargo — strategy	13.07.2026	Logistics	strategy only (+ DQ assessment option)	A 30 wd	independent
OYAK Dijital	08.10.2026	Group / holding	full + technology selection (RFP / POC)	A 9 wk · B 10 + 12 wk · C 12 mo	IDMC
Havelsan	21.09.2026	Defence, technology	full; DQ as sub-option of Phase 2	A 8 wk · B 12 + 10 wk · C 12 mo	on-prem
Memorial	25.09.2026	Healthcare	strategy + process and data-flow analysis	A 12 wk	independent
Kazanci Holding	08.10.2026	Group / energy	rollout of installed IDMC, 4 domains	B 12 wk	IDMC
THY	18.09.2026	Aviation	migration on-prem to IDMC + training	B 62 wd	on-prem to IDMC
Vakifbank	08.10.2026	Banking	catalogue and lineage only	B 80 wd	EDC (on-prem)
Penti — customer deck	12.10.2026	Retail	Assessment / Strategy / Enablement / Managed	indicative W0–W16	IDMC, CLAIRE

TRIGGERS SEEN IN THE SOURCES

DG programme RFP
OYAK Dijital

Group with subsidiaries
OYAK, Kazanci, Aras

On-prem to cloud move
THY

Installed tool, low use
Kazanci

AI plans need trusted data
Penti, OYAK

Scope Boundary and Adjacent Services

What the programme does not do, and the Komtaş services it links to without absorbing them.

KOMTAS

01 · BOUNDARY

OUT OF SCOPE · SOURCE PROPOSALS §15

- Hardware, cloud infrastructure, OS, database and network: supply and operation
- Development or fixes in source systems
- Historical data cleansing, correction and data migration
- Legal opinion and KVKK compliance audit — work is limited to technical and process alignment
- Internal audit, external audit and regulator submissions
- A separate dashboard or BI tool — built-in platform dashboards are used in B
- In A: installing a catalogue or DQ platform (that is B)
- In group customers: simultaneous roll-out to all group companies

ADJACENT SERVICES · LINKED, NOT INCLUDED

Operational Data Governance Enablement

governance at creation and at change in operational systems; extends this programme to the source

AI Governance Readiness

model and use-case governance; builds on ownership, classification and DQ from this programme

Data Product Delivery

data products with owner, contract and SLO; uses glossary, catalogue and DQ from B

Data Mesh Readiness

federated operating model; starts from the DG organisation (category 1)

DWH / Lakehouse Assessment

architecture assessment; here category 3 is scored, not redesigned

Informatica licence

IPU or Axon / EDC / IDQ licences in a separate proposal («LICENCE PROPOSAL REF»)

Boundary with Operational Data Governance. This programme designs the six standard processes, including new data creation in the database. Checks at the point of entry and the gate on the release path are delivered by the Operational Data Governance package.

SECTION 2

Method

The ten-category maturity model is the spine. Three pillars and one operating model turn the assessment into a programme.

The ten-category maturity model — p. 8

Level descriptors 1–5 per category — p. 9 – 10

How maturity is measured and what it produces — p. 11

Three pillars · operating model and six standard processes — p. 12 – 13

The Spine — Ten-Category Maturity Model

KOMTAS

First work package of A: each category scored at current and target level 1–5, with gap and improvement actions. Source: Aras Kargo §4.4, same in OYAK, Havelsan.

02 · MATURITY MODEL

1 DG organisation

roles, committees, decision mechanisms, ownership model, escalation

2 Policies, standards, processes

existence, currency, applicability and follow-up of written policies

3 Data architecture

source system inventory, integration topology, fit with target architecture

4 Metadata and data catalogue

technical and business metadata coverage, catalogue use, lineage visibility

5 Data quality

critical data elements, quality dimensions, rule sets, measurement and reporting

6 Master and reference data

golden record definition, de-duplication, reference data management and distribution

7 Data security and privacy

classification, access control, KVKK compliance, personal data inventory

8 Data lifecycle

creation, retention, archiving and disposal policies and how far they are applied

9 Analytics and data use

reporting discipline, single metric definitions, self-service maturity

10 Culture, awareness, competence

data literacy, training level, adoption and change management

MAIN PILLAR: organisation and roles | policies and processes | data and technology

Output per category: current level · target level (agreed with the customer) · gap · improvement actions → roadmap in short, medium and long term

Level Descriptors 1–5 — Categories 1 to 5

KOMTAS

Derived from the source focus areas (§4.4). Komtaş working descriptors; a level is reached when its description holds for the scope assessed.

draft — delivery to confirm

CATEGORY	1 INITIAL	2 DEVELOPING	3 DEFINED	4 MANAGED	5 OPTIMISED
1 DG organisation	No named roles; data decisions made case by case by IT or the requester.	Some owners named informally; no committee; escalation by personal contact.	DG office, owner, steward and custodian roles defined; committee meets on a schedule.	Roles staffed per domain; decisions and escalations recorded and tracked.	Model works across units or group companies; roles reviewed periodically.
2 Policies, standards, processes	No written DG policy; practice depends on individuals.	Some policies exist but are outdated or not followed.	Policy, procedures and the six standard processes approved; RACI in place.	Compliance monitored; exceptions decided by the committee.	Policies reviewed periodically and changed on measured results.
3 Data architecture	No source system inventory; integrations undocumented.	Partial inventory; integrations known to a few people.	Complete inventory and integration topology documented.	Changes checked against the target architecture.	Architecture decisions governed and traced to business needs.
4 Metadata and catalogue	No catalogue; metadata in spreadsheets or in people's heads.	Technical metadata scanned for some systems; no business link.	Priority systems catalogued; terms linked to physical assets.	Lineage and impact analysis used before changes; scans scheduled.	Catalogue is the default entry point to data; kept current.
5 Data quality	Problems found by report users; no rules.	Ad hoc checks in some projects; no CDE list.	CDEs, dimensions and rule templates defined; thresholds set.	Rules run on schedule; scorecards reviewed by owners.	Issues traced to root cause and fixed at source.

Level Descriptors 1–5 — Categories 6 to 10

KOMTAS

Same scale. Target levels are agreed with the customer per category; no default target is proposed in advance.

draft — delivery to confirm

CATEGORY	1 INITIAL	2 DEVELOPING	3 DEFINED	4 MANAGED	5 OPTIMISED
6 Master and reference data	Same entity held differently in each system; duplicates common.	Duplicates known; local clean-ups; reference lists copied by hand.	Golden record rules and reference data owners defined.	Matching and reference data distribution managed centrally.	Master and reference data governed across all consuming systems.
7 Security and privacy	No classification scheme; location of personal data unknown.	Personal data inventory started for KVKK; access granted on request.	Classification scheme and personal data inventory structure defined.	Sensitive data tagged in the catalogue; access follows the class.	Classification and access controls reviewed and evidenced regularly.
8 Data lifecycle	No retention or disposal rules; data kept indefinitely.	Retention rules for some data, applied manually.	Creation, retention, archiving and disposal policies written.	Policies applied and checked per system.	Lifecycle steps automated and audited.
9 Analytics and data use	Same metric calculated differently across reports.	Key metrics agreed in some units; reports built by IT on request.	Metric definitions in the glossary; reporting standards set.	One definition used across reports; certified datasets for self-service.	Self-service on governed data is the norm.
10 Culture, awareness, competence	Data seen as an IT matter; no training.	Awareness sessions held once; interest depends on individuals.	Role-based training plan; owners and stewards trained.	Adoption measured; DG part of the objectives of key roles.	Data literacy embedded; change managed through the DG office.

How Maturity Is Measured — and What It Produces

KOMTAS

Structured interviews, workshops, document review and technical inventory analysis. The report is the first deliverable of A, in week 2.

02 · MEASUREMENT

INPUTS

Structured interviews

business units, data owners, application owners, IT, information security, internal audit; up to «N» units (6 in Aras, up to 10 in OYAK)

Awareness workshop

executive session and a session open to all; material handed over

Document review

existing policies, procedures and process documents

Technical inventory

system inventory, technical metadata and environment information from IT / data architecture


STEPS · CURRENT-STATE ANALYSIS, 10 WORKING DAYS IN PLAN

1. **Score current level**
   per category, with evidence from interviews and documents
2. **Agree target level**
   with the customer, per category
3. **Gap analysis**
   current against target
4. **Improvement actions**
   feed strategy, framework and roadmap

Plan in the sources: interviews 5 d · awareness workshop 2 d · current-state report 3 d

OUTPUT · MATURITY PROFILE

illustrative

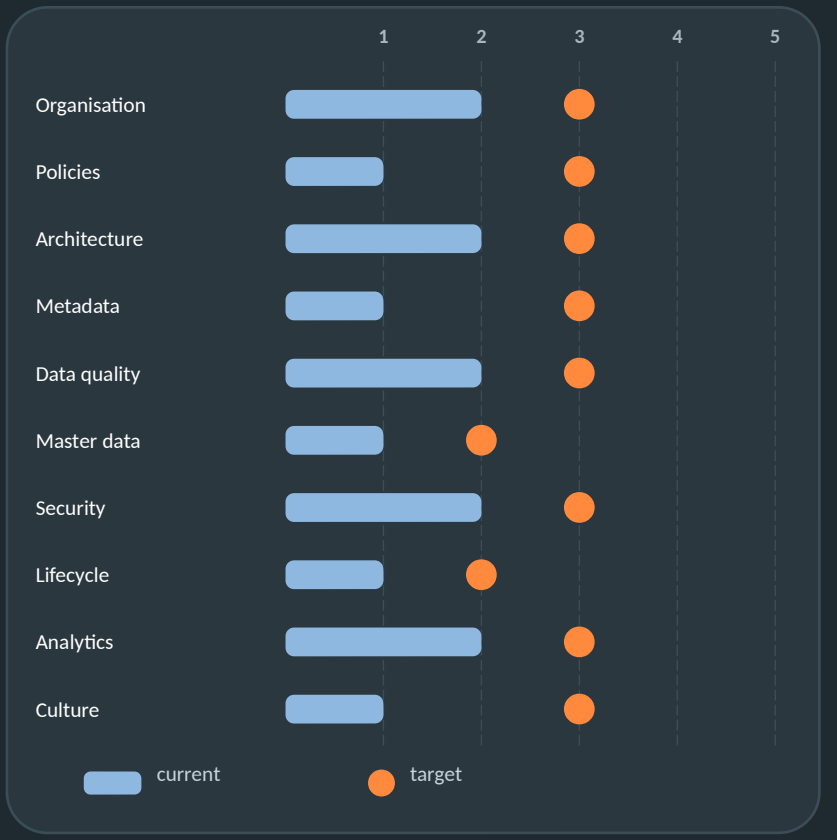

Draft, feedback, final. Every main deliverable is shared as a draft; the customer's feedback is applied, then the final version is submitted for approval. Review period: «N» working days (10 in the sources).

Three Pillars — Organisation, Policies, Technology

KOMTAS

The structure rests on three pillars. The programme succeeds only when all three are built together and support each other (source §4.1).

02 · THREE PILLARS

Organisation and roles

defines who decides

- DG office, owner, steward, custodian
- committee structure
- decision, approval and escalation
- central standard vs local flexibility in groups

A3 · categories 1, 10

Policies and processes

standardises behaviour

- DG policy and procedures
- six standard processes
- role-based RACI
- glossary, DQ and classification templates

A4 · A5 · categories 2, 7, 8

Technology

makes it visible and measurable

- business glossary and data dictionary
- catalogue, lineage, impact analysis
- sensitive data tagging
- DQ rules, scorecards, dashboards

B1 · B2 · B3 · categories 3–6, 9

WHAT GOES WRONG WITH ONE PILLAR ONLY

Policies and processes only
The framework is hard to carry into daily operations and into scalable practice.

Technology only
Without ownership, processes and decision rights, use and adoption are at risk.

Order of the phases. A builds the organisation and the written set and proves them in a pilot; B puts them on the platform; C keeps them running. The pilot in A is the bridge between the pillars.

Operating Model — Roles, Committees, Six Standard Processes

KOMTAS

Designed in A3 and A4, configured on the platform in B1. Decision, approval and escalation follow the same chain in every process.

ROLES

DG office
runs the programme; owns standards, templates and the platform; first audience of the platform workshop

Data owner
accountable for a domain's data; approves terms, rules and thresholds; usually a business manager

Data steward
maintains terms, rules and issues day to day; first contact for data questions

Data custodian
technical data steward: systems, storage, access and scans

DG committee
meets periodically; decides on cross-domain questions and escalations

DECISION AND ESCALATION

Data steward

↓

Data owner

↓

DG committee

↓

Sponsor / steering committee

Group customers: central standard set by the holding, local flexibility per subsidiary.

THE SIX STANDARD PROCESSES · WITH RACI

1. New data creation in the database
2. New glossary term (data element)
3. Periodic glossary review
4. DG committee periodic meeting
5. DQ rule definition
6. DQ measurement and monitoring

on the platform: approval workflow for domain, business term and metric (B1)

RACI per process and role. Roles and responsibilities are set from the customer's current processes and statements; the customer takes an active part. The same roles are created on the platform in B1, so the written model and the tool match.

SECTION 3

Tiers

A Strategy & Framework, B Technology Enablement, C Managed Service. Each tier can be sold on its own.

Three tiers at a glance — p. 15

A — work packages, deliverables, plan and optional blocks — p. 16 – 17

B — modules B1 / B2 / B3 and the two platform blocks — p. 18 – 19

B variants — Migration and Rollout — p. 20

C — MSU model, SLA and service catalogue — p. 21 – 22

Three Tiers — A Strategy & Framework, B Technology Enablement, C Managed Service

KOMTAS

A designs and proves, B implements on Informatica, C operates and extends. A decision point sits between the tiers.

03 · TIERS

A — Strategy & Framework

6–12 weeks · product-independent

Focus	maturity, organisation, policies, templates, pilot, roadmap
Basis	DAMA-DMBOK, COBIT, KVKK
Output	framework, RACI, templates, roadmap; optional technology selection
Pricing	fixed price; 10 / 30 / 30 / 30

B — Technology Enablement

8–16+ weeks · Informatica

Focus	glossary, catalogue, lineage, tagging, data quality
Structure	B1 / B2 / B3; IDMC or on-prem; Migration, Rollout
Output	configured platform, documents, workshops; training optional
Pricing	fixed price per module; 20 / 40 / 40

C — Managed Service

12 months · optional

Focus	operate and extend DQ and DG on demand
Unit	«N» MSU per month; 26-item catalogue
Output	rules, terms, metadata, issues by priority
Pricing	annual fee; monthly MSU

Each tier sells on its own. A only: strategy proposals (Memorial, Aras July). B only: tool already chosen or installed (Kazanci, THY, Vakifbank). Licences are always a separate proposal.

A — Strategy & Framework: Work Packages and Deliverables

KOMTAS

Seven work packages from the source (§5.1.1–5.1.7). Deliverable weeks as in the six-week Aras plan; deliverables 8–9 only when technology selection is in scope.

WORK PACKAGES

#	WORK PACKAGE	CONTENT
A1	Maturity assessment	10 categories; up to «N» unit interviews; document review; current and target level, gap
A2	Awareness sessions	executive and general sessions; material handed over
A3	Strategy, framework, organisation	vision, principles, framework; roles, committees; decision and escalation
A4	Policies, processes, RACI	DG policy and procedures; six standard processes; role-based RACI
A5	Glossary, metadata, DQ templates	glossary and dictionary structure; DQ dimensions, rule templates, thresholds, frequency; classification scheme; personal data inventory
A6	Pilot on the platform	one domain: terms and ownership, roles, sample DQ rules and results
A7	Roadmap	short, medium and long term; technology requirements

DELIVERABLES

#	DELIVERABLE	WEEK
1	Maturity assessment report	2
2	Organisation model and role definitions	3
3	Strategy and target framework	4
4	RACI matrix	5
5	Glossary and DQ rule templates	5
6	DG policy and procedure	5
7	Roadmap and closing report	6
8	Technology requirements and criteria set	opt.
9	RFI / RFP draft for selection	opt.

PAYMENT · A

10% kick-off	**30%** organisation model and roles	**30%** policies and procedures	**30%** pilot and roadmap

Variant seen: 20 / 30 / 30 / 20 (Memorial, Aras July).


A — Plan, Pilot Boundary and Optional Blocks

KOMTAS

The base plan is 30 working days. Optional blocks extend A when the customer needs them; each is priced on top of the base.

03 · TIER A

BASE PLAN · 30 WORKING DAYS (ARAS KARGO)

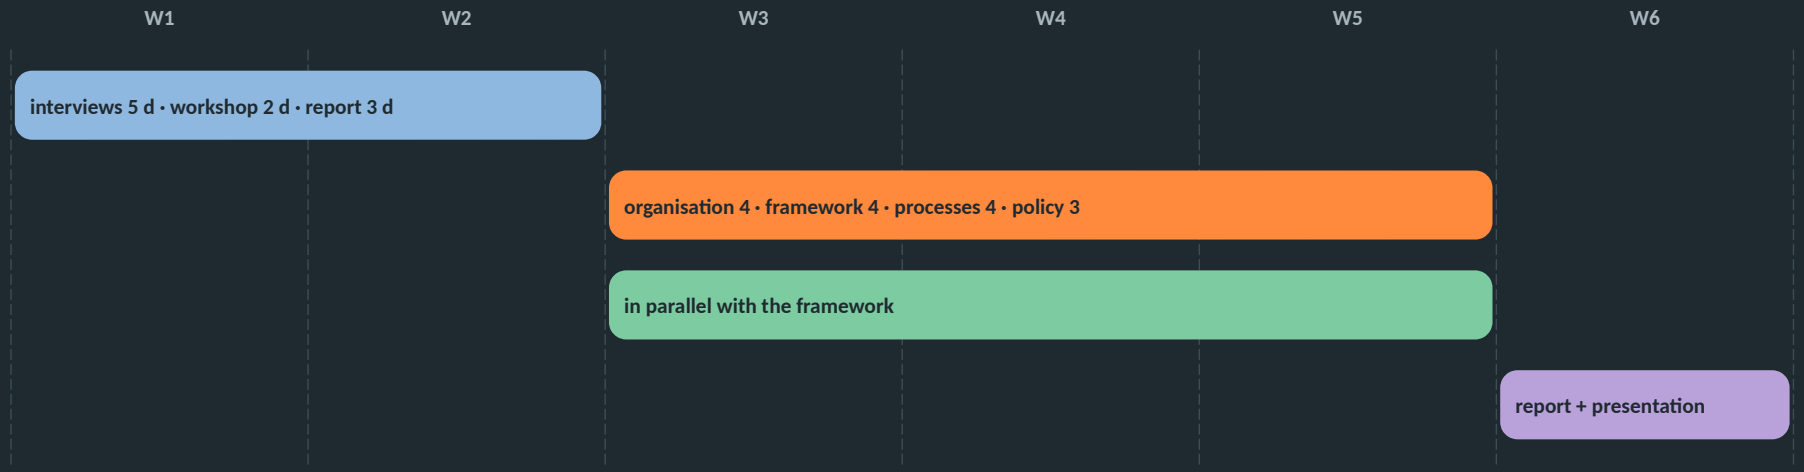

OPTIONAL BLOCKS

Technology selection support

OYAK Dijital

requirements and evaluation criteria, vendor pre-assessment, RFI / RFP technical criteria, POC scenarios, final vendor evaluation; A grew to 45 wd

Process and data-flow analysis

Memorial

end-to-end flow of a priority data set; bottlenecks and manual steps; data kept outside systems (Excel, local files); where the data should be held

DQ assessment on a sample

Aras July

sample DQ analysis on real data gives a concrete indication of current quality; 10 pd, 10 days

Pilot boundary. Access and data provided for the pilot are used for the pilot only. Permanent operation of the platform, continuous data feeds and production operation are out of scope of A and belong to B.

B — Technology Enablement: Modules B1, B2, B3

KOMTAS

Each module has its own scope, plan, deliverables, fee table and payment table (Aras commercial pattern). Base = one domain. Scope limits are «N» fields in the template.

MODULE	SCOPE	LIMITS SEEN IN THE SOURCES	DURATION	PAYMENT 20 / 40 / 40
B1 Business glossary and data dictionary	terms for «DOMAIN»; domain, subdomain, business term, metric; approval workflow; roles and SSO; terms linked to physical metadata	1 domain; customer business units fill the template, Komtaş enters it on the platform	~4 wk	start · glossary live
B2 Catalogue, lineage and classification	scans of «SOURCE SYSTEMS»; up to «N» tables and «N» reports; impact analysis; sensitive data tagging on «SYSTEM», «N» terms, «N» sample records	Aras 4 sources, 2,500 tables / 500 reports; Havelsan 3 DB + 2 ETL/BI, 1,000 / 500; tagging 1 system, 10 terms, 10,000 sample records	~7 wk	start · catalogue ready
B3 Data quality	profiling, rules, data model, reference libraries, parameter and log structure, scorecards on «SYSTEM»	1 system, ~1,000,000 records, 1 domain, up to 50 terms and 100 rules; reference library up to 10,000 rows	~8 wk, parallel	start · rule docs · handover

COMMON TO ALL MODULES

Workshops
platform workshop for the DG office; end-user workshop for business units

Training (optional)
for Developers: digital 10 h, 6 months, or classroom 2 days, max 15

Support (optional)
«N» months after go-live; OYAK: 3 months, up to 2 days a week

DELIVERABLES

- Technical design
- DQ rules document
- Test scenarios
- End-user document
- Technical operations document
- Operational manual
- SMX document (IDMC)

Not in B3: cleansing, matching and de-duplication. Scans and tagging run in batch, weekly or monthly.

B — Two Platform Blocks: IDMC or On-Prem

KOMTAS

Templates carry both blocks, marked «PLATFORM BLOCK — IDMC» and «PLATFORM BLOCK — ON-PREM». The block not used is deleted.

03 · PLATFORM BLOCKS

CAPABILITY	Block 1 · Informatica IDMC (cloud)	Block 2 · Informatica on-prem (on-prem)
Glossary and governance	Cloud Data Governance and Catalog (CDGC)	Axon
Catalogue and lineage	CDGC + Metadata Command Center	Enterprise Data Catalog (EDC)
Data quality	Cloud Data Quality (CDQ)	Informatica Data Quality (IDQ)
Runtime at customer	Secure Agent on a customer server	servers provided by the customer
Identity	SAML SSO, e.g. Azure AD «IDENTITY PROVIDER»	LDAP
Licence metric	IPU, consumption-based	Axon users · EDC resources · IDQ cores
Training	CDGC / CDQ for Developers	Axon / EDC / IDQ for Developers
Seen in	Aras, OYAK, Kazanci, THY (target)	Havelsan, Vakifbank, THY (source)

Licence stays outside. Licence pricing is not in the templates; one sentence refers to «LICENCE PROPOSAL REF». Hardware, OS, database and network for the platform are provided by the customer.

B Variants — Migration and Rollout

Described inside the B template as alternative scope blocks, not as separate files. Calibrated separately from the S / M / L bands.


03 · B VARIANTS

Migration

THY pattern

On-prem Axon / EDC / IDQ moved to IDMC

Terms	«N» (THY: 6,500)
Sources	«SOURCE INVENTORY» (THY: Oracle, Teradata, DataStage, MSTR, MSSQL, Couchbase custom)
DQ rules	«N» (THY: 370)
API	«N» integrations (THY: 1, standard complexity)

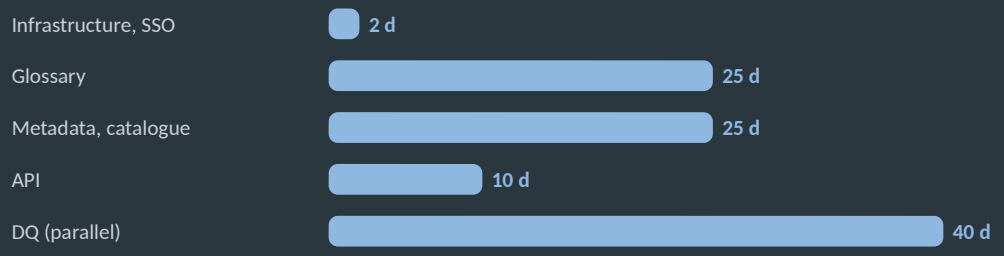

62 wd in plan · 95–106.8 pd

Rollout

Kazanci pattern

Installed IDMC extended to new domains in waves

- reuse pilot outputs as the standard, do not rebuild
- select domains by business value, criticality, DQ problems, analytic use, technical access
- minimum viable governance per domain, deepened through a backlog
- assets managed on IDMC; Excel only for collection
- templates from one wave reused in the next

Preparation	Domain analysis	IDMC implementation	Operationalisation
backlog, Definition of Done	scope, priority assets	terms, catalogue, DQ	dashboards, workflow, next backlog

12 wk per wave of 4 domains · up to 150 terms and 400 rules per domain · effort not written

Vakifbank shape. Catalogue and lineage only on EDC (12 Oracle and 11 MSSQL databases, 40 PowerCenter projects, SAP BO 45,000 reports, Qlik 500 reports) is B2 alone at L scale; no separate variant.

C — Managed Service: MSU Model and Service Levels

KOMTAS

Demand-based service for data quality and data governance after go-live. 150 MSU per month in all observed proposals.

03 · TIER C

HOW MSU WORKS

12 months
from contract start

«N» MSU per month
capacity; MSU = relative size and complexity of a catalogue item

Roll-over
unused MSU moves to the next months


Extra MSU
can be bought when the package is not enough

Free allocation
capacity used across catalogue items by customer priority

No monthly guarantee
work planned by priority, dependency and MSU use

EXAMPLE MONTH · 150 MSU

illustrative



3 simple DQ rules	30 MSU
1 complex DQ rule	30 MSU
1 scorecard	20 MSU
20 glossary terms	20 MSU
1 policy added	50 MSU

ENTRY OPTION · HYPERCARE

«N» months after go-live (OYAK: 3 months, up to 2 days a week): questions and issues in use, analysis and fixes, new needs assessed.

SERVICE LEVELS

P1 critical — full outage, operation stopped; 7×24	**1 hour**
P2 high — major outage or serious performance loss	**4 hours**
P3 low — no operational impact; questions	**next business day**

Support hours Monday–Friday 08:00–17:00, local holidays excluded. Channels: phone, Komtaş support portal, e-mail.

NOT IN SUPPORT (§13): on-site work · unordered installs and upgrades · third-party software and hardware · performance, capacity, security administration · backup, restore, DBA · data migration, integration, custom programming · product training

C — MSU Service Catalogue (26 Items)

KOMTAS

Kept verbatim from the source (Aras Kargo §5.3; same in OYAK and Havelsan), translated. MSU values are agreed with the customer in the proposal.

DATA QUALITY · 14 ITEMS

ACTIVITY	DESCRIPTION	MSU
DQ rule business definition	define the DQ business rule	10
DQ rule technical design	turn the business rule into technical logic	10
DQ rule template	create a reusable rule	10
DQ rule, simple	null / format check	10
DQ rule, medium	cross-field validation	20
DQ rule, complex	validation across several tables	30
AI / anomaly DQ rule	advanced anomaly detection	50
Rule execution set-up	configure rule execution	10
Threshold definition	set acceptance thresholds	10
Scorecard	define score metrics	20
Dashboard set-up	build the DQ monitoring dashboard	50
Issue pre-assessment	first analysis of an issue	10
Root cause analysis	find the root cause	20
Data standardisation flow	correct the target data	50

DATA GOVERNANCE · 12 ITEMS

ACTIVITY	DESCRIPTION	MSU
Glossary terms (10)	define 10 business terms	10
Term relationship mapping	link terms to assets	10
Glossary approval workflow	define the term approval lifecycle	50
Glossary domain	create the domain structure	20
Add a policy	add a governance policy	50
Define a standard	define a standard	20
Data steward onboarding	support a data steward	10
Governance meeting	hold a governance meeting	10
Issue management	follow governance issues	50
Metadata of another system	catalogue technical metadata	100
Metadata enrichment	add business metadata	20
Impact analysis extension	configure impact analysis	20

SECTIONS 4 – 5

Delivery Economics and Package Status

Bands calibrated on proposal plans, team, internal fee references and payment patterns. All efforts are plan-based — to be updated with actual effort from delivery.

Bands S / M / L and their drivers p. 24

Calibration — the source proposals p. 25

Team and effort split by role p. 26

Internal fee references and payment patterns p. 27

Package files and open items p. 28

Bands S / M / L and Their Drivers

KOMTAS

Internal bands calibrated on proposal plans. Plan-based — to be updated with actual effort from delivery.

BANDS

TIER	BAND	DURATION	EFFORT (PD)	CALIBRATED ON
A	S	30 wd (6 wk)	40–50	Aras (30 wd); Aras July 39 pd
A	M	40–45 wd (8–9 wk)	80–90	Havelsan 40 wd / 84 pd; OYAK 45 wd
A	L	60 wd (12 wk)	110–120	Memorial 60 wd / 116 pd
B	S	~42 wd (8 wk)	~100	Aras
B	M	52–61 wd (10–12 wk)	120–165	OYAK; Havelsan 92 + 74 pd
B	L	80+ wd (16+ wk)	170+	Vakifbank scale
C	S	12 months	100 MSU / mo	—
C	M	12 months	150 MSU / mo	all observed proposals
C	L	12 months	200+ MSU / mo	—

DRIVERS · A

plan-based

DRIVER	S	M	L
Unit interviews	≤6	7–10	>10
Pilot domains	1	1	2+
Legal entities	1	2–3	>3
Technology selection	no	yes	yes
Extra analysis blocks	none	1	2+

DRIVERS · B (base: 1 domain, B1 + B2 + B3)

DRIVER	S	M	L
Source systems	≤4	5–6	>6
Tables	≤1,000	≤2,500	>2,500
Reports	≤500	≤500	>500
Domains	1	1	2+
DQ rules	≤100	≤200	>200

Band rule.
The band is the highest band reached by at least three drivers.

Module split (Aras commercial).
B1 ~4 wk · B2 ~7 wk · B3 ~8 wk, B3 in parallel. Variants: Migration 62 wd / 95–107 pd; Rollout 12 wk per wave of 4 domains.

Calibration — The Source Proposals

KOMTAS

Durations and effort as written in each proposal. Where effort is not written, the cell says so; Aras figures in brackets are SAT readings of the plan allocations.

plan-based — to be updated with actual effort from delivery

PROPOSAL	DATE	SHAPE	A DURATION	A EFFORT (PD)	B DURATION	B EFFORT (PD)	C	BAND
Aras Kargo	02.10 / 06.10.2026	full, modular	30 wd (6 wk)	not written (~35–45)	42 wd (8 wk)	not written (~95–105)	150 MSU	A-S · B-S · C-M
Aras Kargo strategy	13.07.2026	strategy only	30 wd	39 (+10 DQ opt.)	—	—	—	A-S
OYAK Dijital	08.10.2026	full + selection	45 wd (9 wk)	not written	52 wd + 60 wd support	not written	150 MSU	A-M · B-M · C-M
Havelsan	21.09.2026	full, DQ option	40 wd (8 wk)	84	61 wd DG + 50 wd DQ	92.2 + 73.6	150 MSU	A-M · B-M · C-M
Memorial	25.09.2026	strategy + analysis	60 wd (12 wk)	116	—	—	—	A-L
Kazanci Holding	08.10.2026	rollout, 4 domains	—	—	12 wk	not written	—	Rollout
THY	18.09.2026	migration	—	—	62 wd (52 in fee table)	95–106.8	—	Migration
Vakifbank	08.10.2026	catalogue + lineage	—	—	80 wd	not written	—	B-L scale
Penti (deck)	12.10.2026	indicative	W2–5 + W5–9	—	W8–13	—	W11–16	—

What the numbers are
proposal plans: working days from the project plan tables and person-days from the effort tables. None is an actual from a delivered project.

What is missing
actuals from delivery for A and B; effort for Aras and OYAK; per-wave effort for Rollout. Collected as open item S4 (p. 28).

Team and Effort Split by Role

KOMTAS

Roles and allocations from the source plans. Effort split where the proposal writes it; plan-based — to be updated with actual effort from delivery.

ROLES

plan-based

ROLE	RESPONSIBILITY	A	B	VARIANTS
Project Manager	plan, scope, risk, change, communication; reporting (10–20%)	○	○	○
DG Partner	strategy direction and management presentation (20%)	○	—	—
DG Team Leader / Senior DG Consultant	method, framework and organisation design, deliverable quality	●	●	●
DG Consultant / Specialist	interviews, maturity scoring, policies, processes; glossary and catalogue build	●	●	●
DQ Team Leader	DQ analysis, rules and controls, follow-up of outputs	—	●	●
DQ Consultant / Specialist	CDEs, DQ rules, glossary and metadata standards; DQ build	opt.	●	●
Support Engineer	Secure Agent install, SAML / SSO (migration)	—	—	●

● main role ○ part time — not needed opt. optional DQ assessment

EFFORT SPLIT AS WRITTEN (PD)

PROPOSAL	PM	SENIOR	TEAM LEAD	SPECIALIST	TOTAL
Aras July — A	3	—	12	24 (+10 DQ)	39 (+10)
Havelsan — A	4	8	32	40	84
Memorial — A	6	10	40	60	116
Havelsan — B DG	12.2	—	20	60	92.2
Havelsan — B DQ	10	—	13.6	50	73.6

Team statements in the sources.
All team members are full-time Komtaş employees, no subcontractors or freelancers; the team lead has at least 8 years in data governance; the team knows at least 3 DM / DG tools besides Informatica (OYAK); a replacement is at least equivalent and its CV is approved by the customer first.

Internal Fee References and Payment Patterns

KOMTAS

Fees as written in the proposals, excluding VAT. Internal only — not for the customer deck or the templates.

FEES IN THE SOURCES

TIER	PROPOSAL	FEE
A	Aras Kargo	1.20 M TL
A	OYAK Dijital (incl. selection)	2.15 M TL
A	Havelsan	3.08 M TL
A	Memorial (fixed price)	3.19 M TL
A	Aras July (strategy, Damalink)	1.10 M TL + 0.30 M DQ opt.
B	Aras Kargo (glossary + metadata / DQ)	1.95 + 1.75 M TL
B	Aras modular M1 / M2 / M3 / M4	0.65 / 0.825 / 1.45 / 1.75 M TL
B	OYAK Dijital	3.78 M TL
B	Havelsan (+ DQ option)	3.025 M TL + 2.42 M TL
B	Kazanci rollout · Vakifbank	1.62 M TL · 5.40 M TL
B	THY migration (95 pd)	EUR 39,900
C	Aras · OYAK · Havelsan (150 MSU, 12 mo)	1.80 · 1.75 · 1.98 M TL / year

DAY RATES SEEN

internal only

SOURCE	RATE	PROFILE
Memorial T&M	47.3k / 45.65k / 28.05k TL	senior / team lead / specialist
Vakifbank	40k / 25k TL	team lead / consultant
OYAK change requests	30k TL	per person-day

PAYMENT PATTERNS

TIER	SPLIT	MILESTONES / WHERE SEEN
A	10 / 30 / 30 / 30	kick-off · organisation · policies · pilot and roadmap (Aras, OYAK, Havelsan)
A var.	20 / 30 / 30 / 20	Memorial, Aras July
B	20 / 40 / 40 per module	start · glossary live or DQ docs · catalogue ready or DQ handover (Aras, Havelsan)
B var.	10 / 30 / 30 / 30	OYAK, one combined B
C	monthly × 12	annual fee, invoiced monthly

Training is billed separately: digital at order, classroom after delivery. Licence is in EUR and in a separate proposal.

Package Files and Open Items

KOMTAS

Same numbering as the other service packages, with -en / -tr suffixes. Files 1, 2 and 4a / 4b / 4c are ready in English and Turkish; files 0, 3a / 3b / 3c, 5 and 6 come next.

#	FILE	STATUS	NOTE
0	process flow	next	TR + EN
1	data-governance-1-blueprint-en / -tr.pptx	ready	this document
2	data-governance-2-musteri-sunumu-en / -tr.pptx	ready	20-minute main flow + appendix; no customer names, effort or fees
3a / 3b / 3c	input form	next	drivers → bands for A and B
4a / 4b / 4c	proposal templates	ready	A Strategy & Framework / B Technology Enablement / C Managed Service
5	customer question set	next	first questions: group structure, units, installed platform
6	internal question set	next	proposal set S1–S14

OPEN ITEMS

- Actual effort from delivery (S4): all A and B efforts are proposal plans; Aras and OYAK efforts are not written
- Rollout variant: the Kazanci proposal gives no effort; delivery to confirm effort per wave of 4 domains
- Licence stays a separate proposal («LICENCE PROPOSAL REF»); IPU and Axon / EDC / IDQ sizing is not part of this package
- KARE record and references: templates carry «REFERENCES» without names or contacts; confirm which references may be cited
- Catalogue: aday-02 merges into this package (aday-20); aday-13 stays separate as Operational Data Governance Enablement
- Level descriptors 1–5 are Komtaş drafts; validate on the first delivered assessment
